





Name of the work with location.	S.No 1 Construction of lane and drain near jk public school/Lawrence school at Pantirthi w.no.1.
Department/Organization	H&UDD
Executing Agency	Jammu Municipal Corporation
Block/District	Jammu
Estimated Cost	2.67
Total Expdt incurred ending 3/2022	1.84
Project Initiation Year	2021
Date of Completion (MM/YY)	08.11.2021
No of beneficiaries	




Name of the work with location.	S.No 2 Construction of lane / drain from h/o Mohan Lal to h/o Pushap Raj& Link h/o Sanjay allied works W.No. 02.
Department/Organization	H&UDD
Executing Agency	Jammu Municipal Corporation
Block/District	Jammu
Estimated Cost	2.67
Total Expdt incurred ending 3/2022	1.89
Project Initiation Year	2021
Date of Completion (MM/YY)	03.11.2021
No of beneficiaries	

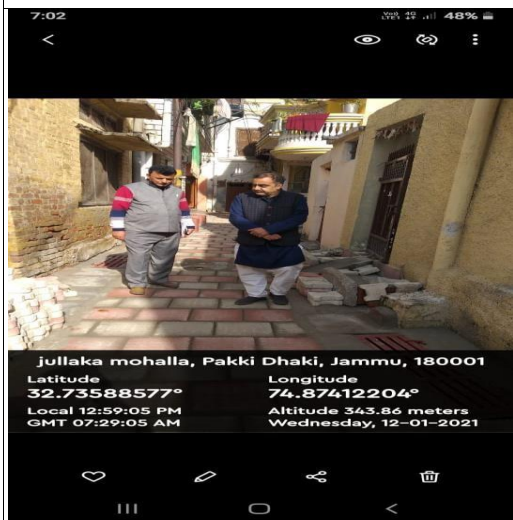

Name of the work with location.	S.No3 Const. Of lane / drain near Peerkho Pully from Bedi residence to Baba Lal Ji road in wno. 03.
Department/Organization	H&UDD
Executing Agency	Jammu Municipal Corporation
Block/District	Jammu
Estimated Cost	2.67
Total Expdt incurred ending 3/2022	1.72
Project Initiation Year	2021
Date of Completion (MM/YY)	15.12.2021
No of beneficiaries	

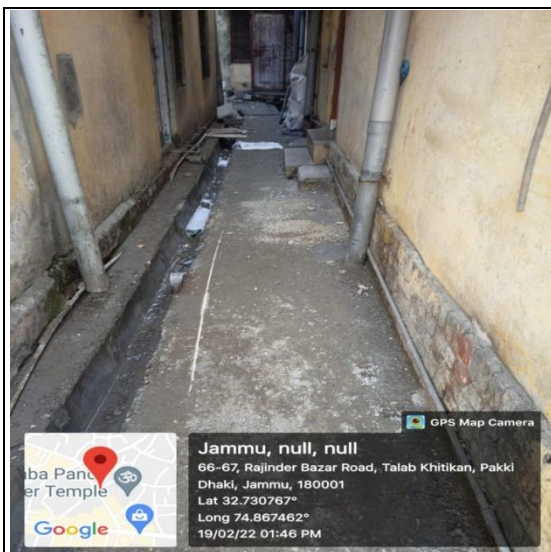

Name of the work with location.	S.No.4 Construction of drain from h/o Smt. Satya Devi to h/o sardar sani (ii) Drain from h/o R.K Razdan to link road Rajinder Bazar (iii) Lande and drain from h/o Bhagi to Link Road Dalpatian Mohalla W No. 05.
Department/Organization	H&UDD
Executing Agency	Jammu Municipal Corporation
Block/District	Jammu
Estimated Cost	2.67
Total Expdt incurred ending 3/2021	2.05
Project Initiation Year	2021
Date of Completion (MM/YY)	05.02.2022
No of beneficiaries	

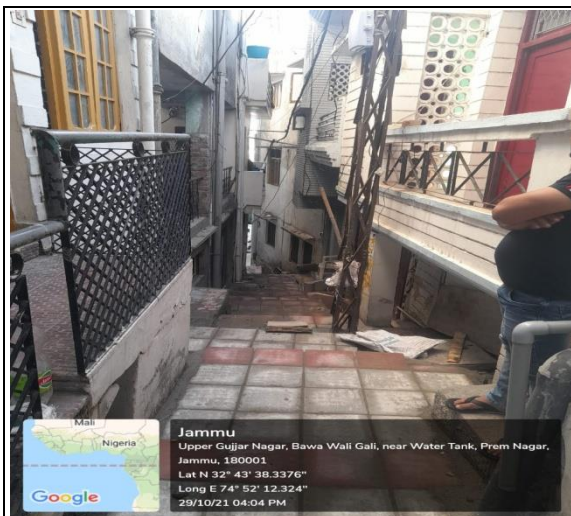

Name of the work with location.	S.No 5 Construction of central drain & steps near h/o Shahnawaz to h/o Roshan Din at WNO. 06.
Department/Organization	H&UDD
Executing Agency	Jammu Municipal Corporation
Block/District	Jammu
Estimated Cost	2.67
Total Expdt incurred ending 3/2022	2.07
Project Initiation Year	2021
Date of Completion (MM/YY)	03.11.2021
No of beneficiaries	




Name of the work with location.	S.No 6 Construction of drain from Sulabh Shouchalaya from Parking old hospital road wno. 10.
Department/Organization	H&UDD
Executing Agency	Jammu Municipal Corporation
Block/District	Jammu
Estimated Cost	2.67
Total Expdt incurred ending 3/2022	1.82
Project Initiation Year	2021
Date of Completion (MM/YY)	02.02.2022
No of beneficiaries	






Name of the work with location.	S.No 7 Construction of defunct drain from h/o sh. Sanjay Kumar Towards Bitta Attachi Prem Nagar WNO. 07.
Department/Organization	H&UDD
Executing Agency	Jammu Municipal Corporation
Block/District	Jammu
Estimated Cost	2.67
Total Expdt incurred ending 3/2022	1.92
Project Initiation Year	2021
Date of Completion (MM/YY)	28.01.2022
No of beneficiaries	

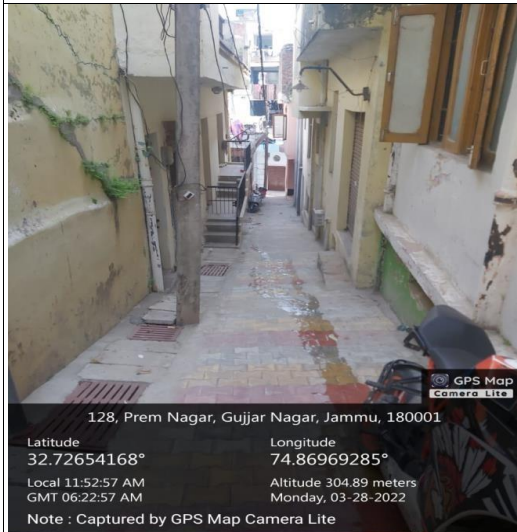


Name of the work with location.	S.No.8 Const. Drain from opp. Trikuta Complex to Gulshan Rahi 54/A Dogra Hall W No. 08.
Department/Organization	H&UDD
Executing Agency	Jammu Municipal Corporation
Block/District	Jammu
Estimated Cost	2.67
Total Expdt incurred ending 3/2022	1.55
Project Initiation Year	2021
Date of Completion (MM/YY)	20.11.2021
No of beneficiaries	



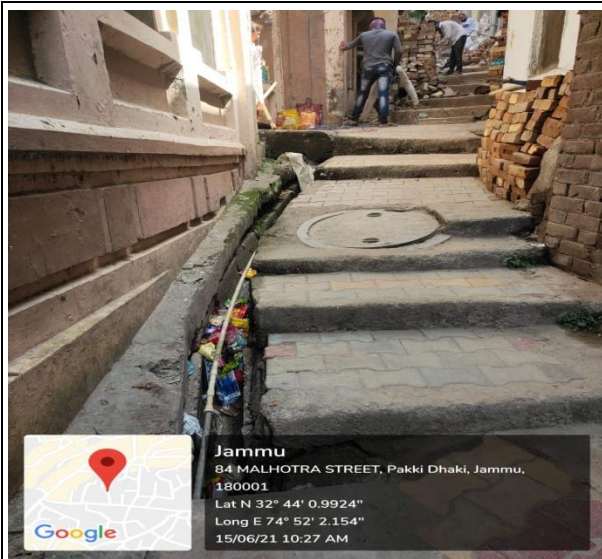

Name of the work with location.	S.No 9 Ex. Hon'ble MLA and railing in steps and const. Of lane near h/o Anand house opp. Hanuman Mandir WNo. 09.
Department/Organization	H&UDD
Executing Agency	Jammu Municipal Corporation
Block/District	Jammu
Estimated Cost	2.67
Total Expdt incurred ending 3/2022	1.70
Project Initiation Year	2021
Date of Completion (MM/YY)	19.03.2022
No of beneficiaries	




Name of the work with location.	S.No 10 Construction of lane /drain from virbhawan to Chemist shop (Maharaja) at Raghunath Pura in wno. 15.
Department/Organization	H&UDD
Executing Agency	Jammu Municipal Corporation
Block/District	Jammu
Estimated Cost	2.67
Total Expdt incurred ending 3/2022	2.51
Project Initiation Year	2021
Date of Completion (MM/YY)	13.11.2021
No of beneficiaries	



	Name of the work with location.	S.No 11 Up gradation of lane from House of Parshotam Lal to Kali Dass..Kacha Talab Bahu Fort wno. 47.
	Department/Organization	H&UDD
	Executing Agency	Jammu Municipal Corporation
	Block/District	Jammu
	Estimated Cost	2.67
	Total Expdt incurred ending 3/2022	1.59
	Project Initiation Year	2021
	Date of Completion (MM/YY)	06.11.2021
	No of beneficiaries	

	Name of the work with location.	S.No 12 Const. Of drain from Noor Masjid to h/o Faid Ali in Chowhadi Ext. D Mohalla Dhalni Wno. 74.
	Department/Organization	H&UDD
	Executing Agency	Jammu Municipal Corporation
	Block/District	Jammu
	Estimated Cost	2.67
	Total Expdt incurred ending 3/2022	1.73
	Project Initiation Year	2021
	Date of Completion (MM/YY)	05.11.2021
	No of beneficiaries	


	Name of the work with location.	Sr.No:13 Remodelling of lane and drain at Christian Colony, Bakshi Nagar Jammu Ward 27
	Department/Organization	JMC Div-II
	Executing Agency	JMC
	Block/District	Jammu
	AA cost (Rs: in Lacs)	2.67
	Total Expdt incurred ending 3/2022	1.64
	Date of start (MM/YY)	27.12.21
	Date of Completion (MM/YY)	31.12.21
	No of beneficiaries	


	Name of the work with location.	Sr.No:14 Fixing Of Grating and Slab At Different Locations Of Ward No; 30 TalabTillo`
	Department/Organization	JMC Div-II
	Executing Agency	JMC
	Block/District	Jammu
	AA cost (Rs: in Lacs)	2.67
	Total Expdt incurred ending 3/2022	1.88
	Date of start (MM/YY)	29.11.21
	Date of Completion (MM/YY)	10.03.22
	No of beneficiaries	

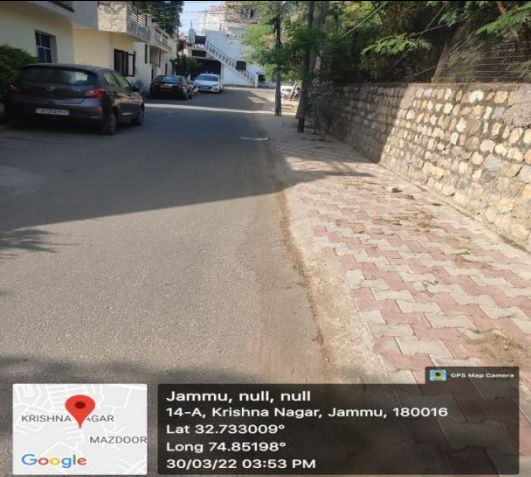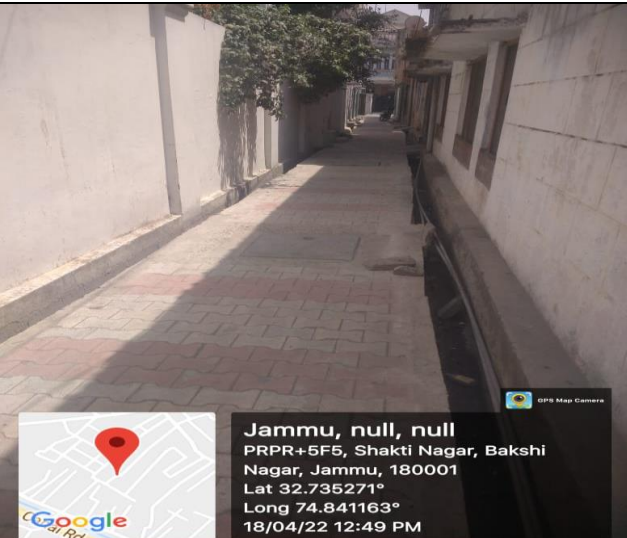


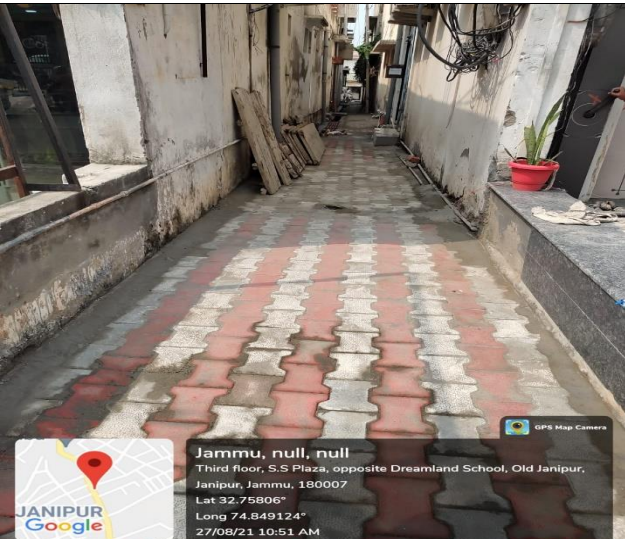
	Name of the work with location.	Sr.No:15 Upgradation of footpath allied works upto H/o Sh. Bindraban Sahni Ward No: 28, Bakshi Nagar
	Department/Organization	JMC Div-II
	Executing Agency	JMC
	Block/District	Jammu
	AA cost (Rs: in Lacs)	2.67
	Total Expendt incurred ending 3/2022	1.66
	Date of start (MM/YY)	27.12.21
	Date of Completion (MM/YY)	31.12.21
	No of beneficiaries	
	Name of the work with location.	Sr.No:16 Repair/upgradation of lanes by W/o 60 mm thick tiles near H/o J.L Raina H.NO; 185-B Khajuria Niwas H.NO; 200/8 Khajuria Cottage H.NO: 227/9 Lane NO; 8 Shakti Nagar ward 29.
	Department/Organization	JMC Div-II
	Executing Agency	JMC
	Block/District	Jammu
	AA cost (Rs: in Lacs)	2.67
	Total Expendt incurred ending 3/2022	1.55
	Date of start (MM/YY)	29.11.21
	Date of Completion (MM/YY)	10.03.22
	No of beneficiaries	





	Name of the work with location.	Sr.No:17 Constt/ renovation of lane from H/o Ajay Kumar to H/o thappa and from H/o Nek ram to H/o Manmohan Singh at B-Block Bhawani Nagar TalbTillo Ward 31
	Department/Organization	JMC Div-II
	Executing Agency	JMC
	Block/District	Jammu
	AA cost (Rs: in Lacs)	2.67
	Total Expdt incurred ending 3/2022	1.54
	Date of start (MM/YY)	20.09.21
	Date of Completion (MM/YY)	25.12.21
	No of beneficiaries	

	Name of the work with location.	Sr.No:18 Providing & fixing of grating/slabs at different locations in ward No: 32
	Department/Organization	JMC Div-II
	Executing Agency	JMC
	Block/District	Jammu
	AA cost (Rs: in Lacs)	2.67
	Total Expdt incurred ending 3/2022	1.81
	Date of start (MM/YY)	20.09.21
	Date of Completion (MM/YY)	25.12.21
	No of beneficiaries	


	Name of the work with location.	Sr.No:19 Repair/upgradation of lanes by lanes with 60 mm paver tiles near H/o Ramesh Sharma H.NO; 239/D lower Shiv Nagar, H/o Omkar Chand H.NO; 541 Lane 10D Lower Shiv Nagar & near H/o Rajesh Sharma H.NO; 40, lane 30 Rajpura
	Department/Organization	JMC Div-II
	Executing Agency	JMC
	Block/District	Jammu
	AA cost (Rs: in Lacs)	2.67
	Total Expdt incurred ending 3/2022	1.54
	Date of start (MM/YY)	25.10.21
	Date of Completion (MM/YY)	15.12.21
	No of beneficiaries	


	Name of the work with location.	Sr.No:21 Upgradation of lane and drain from Lakme Saloon upto H/o Yograj Sharma Opp. Gunjan Plaza Ward 35
	Department/Organization	JMC Div-II
	Executing Agency	JMC
	Block/District	Jammu
	AA cost (Rs: in Lacs)	2.67
	Total Expdt incurred ending 3/2022	1.19
	Date of start (MM/YY)	25.10.21
	Date of Completion (MM/YY)	15.12.21
	No of beneficiaries	


	Name of the work with location.	Sr.No:22 Constt. of lane & drain from H/o Subash Sharma to H/o O.P Thakur (Adv) H/o vijay Kumar to H/o S.K Thapa Shiv Mandir lane Ward 36.
	Department/Organization	JMC Div-II
	Executing Agency	JMC
	Block/District	Jammu
	AA cost (Rs: in Lacs)	2.67
	Total Expdt incurred ending 3/2022	1.87
	Date of start (MM/YY)	25.10.21
	Date of Completion (MM/YY)	15.12.21
	No of beneficiaries	

	Name of the work with location.	Sr.No:23 Upgradation of lane from H/o B.R Manhas to h/o Sh. Vijay Gupta near PHE overhead tank Ward 37 janipur
	Department/Organization	JMC Div-II
	Executing Agency	JMC
	Block/District	Jammu
	AA cost (Rs: in Lacs)	2.67
	Total Expdt incurred ending 3/2022	1.52
	Date of start (MM/YY)	25.10.21
	Date of Completion (MM/YY)	15.12.21
	No of beneficiaries	



	Name of the work with location.	Sr.No:24 Repair of lane and covering of drain from H/o KK Sharma to J.S health Gym at basnat Nagar Ward 38, Janipur
	Department/Organization	JMC Div-II
	Executing Agency	JMC
	Block/District	Jammu
	AA cost (Rs: in Lacs)	2.67
	Total Expdt incurred ending 3/2022	1.99
	Date of start (MM/YY)	25.10.21
	Date of Completion (MM/YY)	15.12.21
	No of beneficiaries	

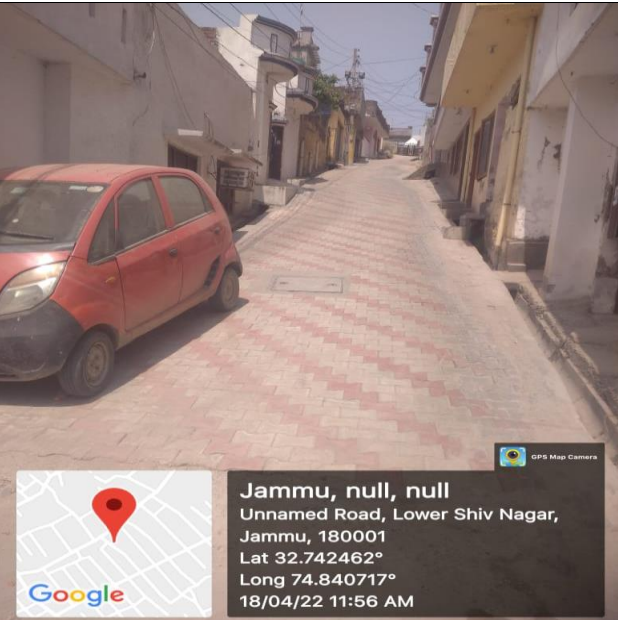	Name of the work with location.	Sr.No:25 Constt. of lane from H/o Sh. Vijay to H/o Ch. Mohinder Ward 39
	Department/Organization	JMC Div-II
	Executing Agency	JMC
	Block/District	Jammu
	AA cost (Rs: in Lacs)	2.67
	Total Expdt incurred ending 3/2022	1.52
	Date of start (MM/YY)	25.10.21
	Date of Completion (MM/YY)	15.12.21
	No of beneficiaries	

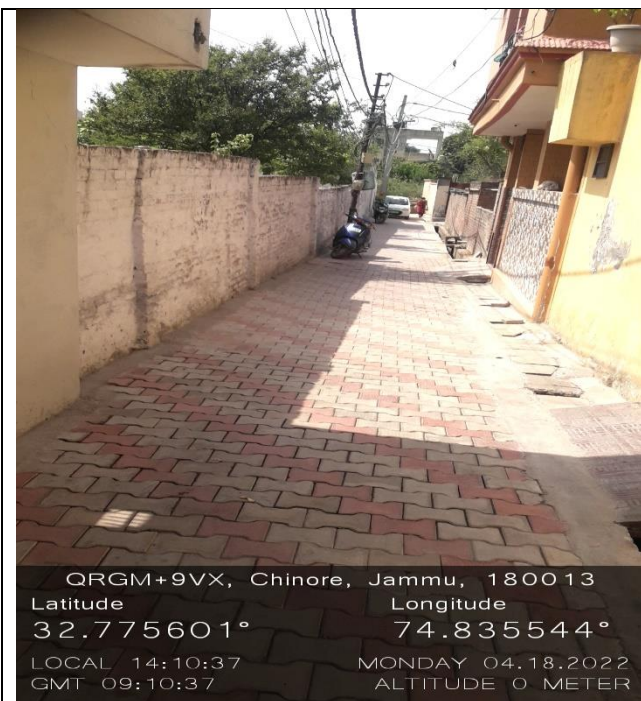

Name of the work with location.	Sr.No:26 Constt. Of Lane From H/O Seva Singh To Rakesh Sharma And From H/O Maksoon To Dogra in Durga Nagar W.No. 40
Department/Organization	JMC Div-II
Executing Agency	JMC
Block/District	Jammu
AA cost (Rs: in Lacs)	2.67
Total Expdt incurred ending 3/2022	1.49
Date of start (MM/YY)	25.10.21
Date of Completion (MM/YY)	15.12.21
No of beneficiaries	




Sr. No.	27
Name of the work with Location	Repair / covering of drain from Hotel Gold Star to New Golden Hotel, Chand Nagar ward No. 19
Department/Organisation	H&UDD
Executive Agency	JAMMU MUNICIPAL CORPORATION DIVISION NO. III
Block/District	JAMMU
AA Cost (Rs . in Lakhs )	2.65
Total Cost of Completion/expenditure incurred ending 3/2022	1.82
Date of Start(Month/Year)	21-10-2021
Date of Completion ( Month / Year)	27-11-2021
No. of beneficiaries	300




Sr. No.	28
Name of the work with Location	Upgradation of lane by way of tiles near H.No. 16 A/C H/o Janak Singh Ward No. 20
Department/Organisation	H&UDD
Executive Agency	JAMMU MUNICIPAL CORPORATION DIVISION NO. III
Block/District	JAMMU
AA Cost (Rs . in Lakhs )	2.65
Total Cost of Completion/expenditure incurred ending 3/2022	1.62
Date of Start(Month/Year)	07-09-2021
Date of Completion ( Month / Year)	25-09-2021
No. of beneficiaries	150



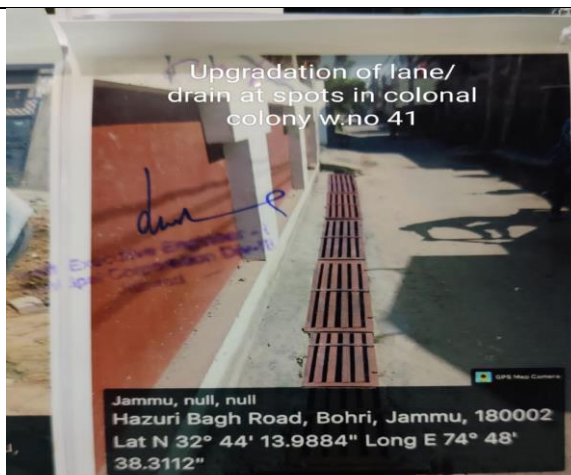

Sr. No.	29
Name of the work with Location	up gradation of lane/drain including steel gratings at spots in Cornol colony ward no 41
Department/Organisation	H&UDD
Executive Agency	JAMMU MUNICIPAL CORPORATION DIVISION NO. III
Block/District	JAMMU
AA Cost (Rs . in Lakhs )	2.65
Total Cost of Completion/expenditure incurred ending 3/2022	1.61
Date of Start(Month/Year)	05-10-2021
Date of Completion ( Month / Year)	30-10-2021
No. of beneficiaries	250

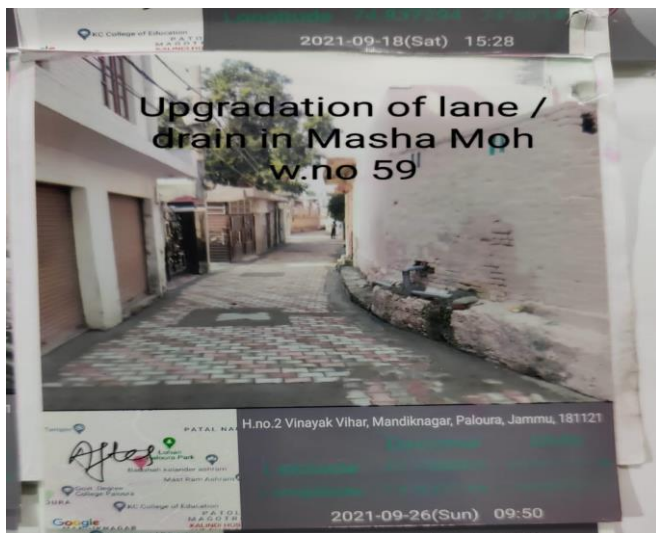

Sr. No.	30
Name of the work with Location	up gradation of lane by w/o laying Paver tiles in Masha Mohalla ward no.59
Department/Organisation	H&UDD
Executive Agency	JAMMU MUNICIPAL CORPORATION DIVISION NO. III
Block/District	JAMMU
AA Cost (Rs . in Lakhs )	2.65
Total Cost of Completion/expenditure incurred ending 3/2022	1.52
Date of Start(Month/Year)	15-09-2021
Date of Completion ( Month / Year)	30-09-2021
No. of beneficiaries	300

# Upgradation of lane / drain in Tammani Moh. nr Tiny Tots School W.no 60




Sr. No.	31
Name of the work with Location	Up gradation of land and drain in Tammani Mohalla near pond Dhok Paloura W.No 60
Department/Organisation	H&UDD
Executive Agency	JAMMU MUNICIPAL CORPORATION DIVISION NO. III
Block/District	JAMMU
AA Cost (Rs . in Lakhs )	2.65
Total Cost of Completion/expenditure incurred ending 3/2022	1.70
Date of Start(Month/Year)	08-09-2021
Date of Completion ( Month / Year)	30-09-2021
No. of beneficiaries	200

**up gradation of lane  
near park in w no 61**




Sr. No.	32
Name of the work with Location	Upgradation of lane at ManormaVihar near Park in ward No. 61
Department/Organisation	H&UDD
Executive Agency	JAMMU MUNICIPAL CORPORATION DIVISION NO. III
Block/District	JAMMU
AA Cost (Rs . in Lakhs )	2.65
Total Cost of Completion/expenditure incurred ending 3/2022	1.60
Date of Start(Month/Year)	30-08-2021
Date of Completion ( Month / Year)	28-09-2021
No. of beneficiaries	300

**up grad lane laxmipuram  
chinoor in w no 62**

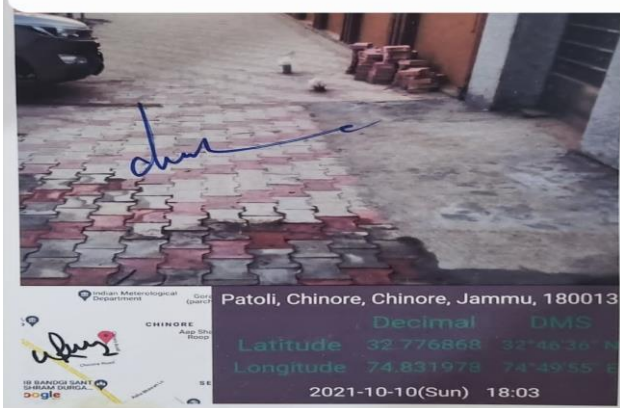

Sr. No.	33
Name of the work with Location	Construction / up gradation of lane by way of laying of paver tiles at Laxmipuram near Maqbool Choudhary in ward No. 62
Department/Organisation	H&UDD
Executive Agency	JAMMU MUNICIPAL CORPORATION DIVISION NO. III
Block/District	JAMMU
AA Cost (Rs . in Lakhs )	2.65
Total Cost of Completion/expenditure incurred ending 3/2022	1.51
Date of Start(Month/Year)	30-08-2021
Date of Completion ( Month / Year)	28-09-2021
No. of beneficiaries	100




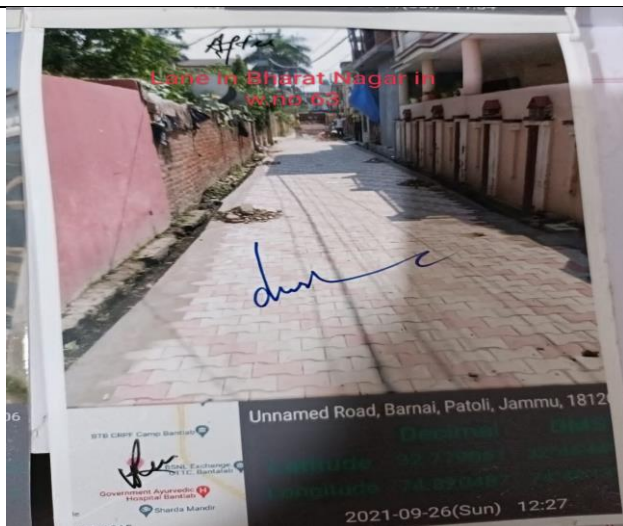


Sr. No.	34
Name of the work with Location	Construction / up gradation of lane at Bharat nagar in ward No. 63
Department/Organisation	H&UDD
Executive Agency	JAMMU MUNICIPAL CORPORATION DIVISION NO. III
Block/District	JAMMU
AA Cost (Rs . in Lakhs )	2.65
Total Cost of Completion/expenditure incurred ending 3/2022	1.51
Date of Start(Month/Year)	30-08-2021
Date of Completion ( Month / Year)	28-09-2021
No. of beneficiaries	100



Sr. No.	35
Name of the work with Location	Upgradation of lane / drain near H/o AmanSansyal near Hanjura lane in ward no. 64
Department/Organisation	H&UDD
Executive Agency	JAMMU MUNICIPAL CORPORATION DIVISION NO. III
Block/District	JAMMU
AA Cost (Rs . in Lakhs )	2.65
Total Cost of Completion/expenditure incurred ending 3/2022	1.51
Date of Start(Month/Year)	30-08-2021
Date of Completion ( Month / Year)	28-09-2021
No. of beneficiaries	140

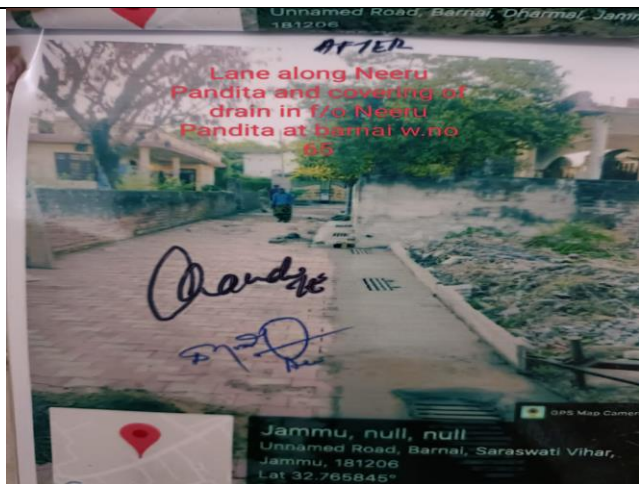

Sr. No.	36
Name of the work with Location	Up gradation of lane along H/o NeeruPandita and covering of drain in front of NeeruPandita at Barnai in ward No. 65
Department/Organisation	H&UDD
Executive Agency	JAMMU MUNICIPAL CORPORATION DIVISION NO. III
Block/District	JAMMU
AA Cost (Rs . in Lakhs )	2.65
Total Cost of Completion/expenditure incurred ending 3/2022	1.64
Date of Start(Month/Year)	16-09-2021
Date of Completion ( Month / Year)	05-10-2021
No. of beneficiaries	160

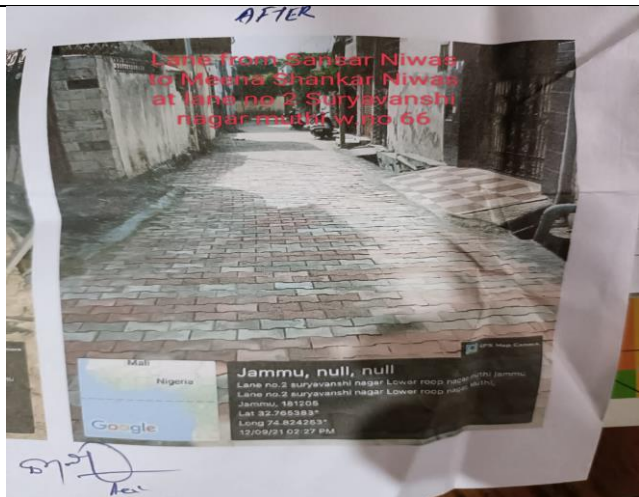

Sr. No.	37
Name of the work with Location	Up gradation of lane from H/o Sansar Niwas at MeenaShanker Niwas at lane No. 2 Suryavanshi Nagar Muthi ward no. 66
Department/Organisation	H&UDD
Executive Agency	JAMMU MUNICIPAL CORPORATION DIVISION NO. III
Block/District	JAMMU
AA Cost (Rs . in Lakhs )	2.65
Total Cost of Completion/expenditure incurred ending 3/2022	1.55
Date of Start(Month/Year)	26-08-2021
Date of Completion ( Month / Year)	15-09-2021
No. of beneficiaries	150



Sr. No.	38
Name of the work with Location	Up gradation of lane along H/o Bobby Dutta at amit Nagar Muthi in ward No. 67
Department/Organisation	H&UDD
Executive Agency	JAMMU MUNICIPAL CORPORATION DIVISION NO. III
Block/District	JAMMU
AA Cost (Rs . in Lakhs )	2.65
Total Cost of Completion/expenditure incurred ending 3/2022	1.51
Date of Start(Month/Year)	29-08-2021
Date of Completion ( Month / Year)	22-10-2021
No. of beneficiaries	160



Sr.no	39
Name of the work with Location	Upgradation of lane drain by way of the precast interlocked tiles from H/o.Handoo Niwas h.no 286 to onwards and allied works near h.no265 in ward no43 under CCDP Head 21-22
Department/Organization	JMC
Executive Agency	JMC
Block /District	JAMMU
AA Cost (Rs in Lakhs)	2.67
Total Cost of Completion/Expenditure Incurred ending 3/2022	1.69
Date of Start Month/Year	8-8-2021
Date of Completion	22-8-2021
No of Beneficiaries	390






Sr.no	40
Name of the work with Location	Covering of drain with grating and RCC Slabs form the H/o. Harjinder singh Hno.40 to Hno.45 at lane no.10 sec-7 Nanak Nagar Jammu ward no. 44
Department/Organization	JMC
Executive Agency	JMC
Block /District	JAMMU
AA Cost (Rs in Lakhs)	2.67
Total Cost of Completion/Expenditure Incurred ending 3/2022	1.90
Date of Start Month/Year	10-9-2021
Date of Completion	8-10-2021
No of Beneficiaries	520




Sr.no	41
Name of the work with Location	Upgradation of lane by way of precast interlock tiles near culvert from H/o. of P.C.Dayal Hno. 150 to onwards in ward no. 45 Preet Nagar under CCDP Head for the year 21-22
Department/Organization	JMC
Executive Agency	JMC
Block /District	JAMMU
AA Cost (Rs in Lakhs)	2.67
Total Cost of Completion/Expenditure Incurred ending 3/2022	1.52
Date of Start Month/Year	15-8-2021
Date of Completion	12-9-2021
No of Beneficiaries	470

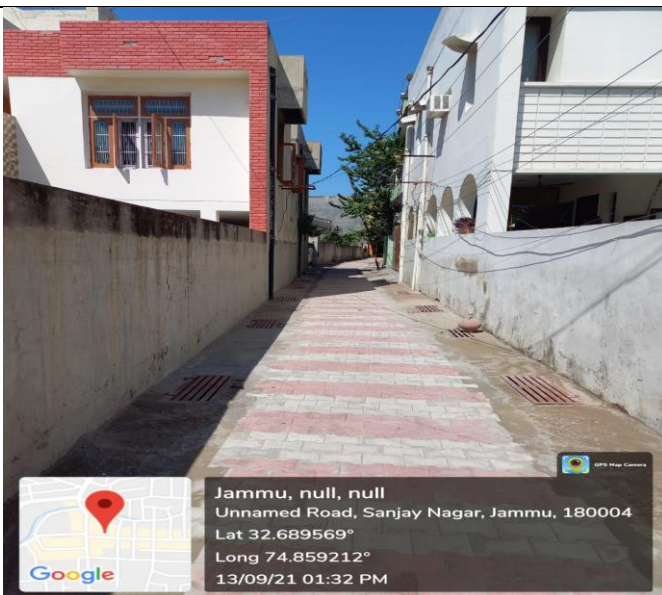

Sr.no	42
Name of the work with Location	Upgradation /repair of lane in H/o. Attar Singh Vali lane & its adjoining lane sec-2 Sanjay Nagar ward no.46
Department/Organization	JMC
Executive Agency	JMC
Block /District	JAMMU
AA Cost (Rs in Lakhs)	2.67
Total Cost of Completion/Expenditure Incurred ending 3/2022	1.57
Date of Start Month/Year	12-8-2021
Date of Completion	11-9-2021
No of Beneficiaries	250



Sr.no	43
Name of the work with Location	Constt./ Upgradation of lane from H/o. Chowdhary to H/o. Anoop Malhotra at South Extn. Trikuta Nagar ward no.52
Department/Organization	JMC
Executive Agency	JMC
Block /District	JAMMU
AA Cost (Rs in Lakhs)	2.67
Total Cost of Completion/Expenditure Incurred ending 3/2022	1.56
Date of Start Month/Year	15-8-2021
Date of Completion	1-9-2022
No of Beneficiaries	190

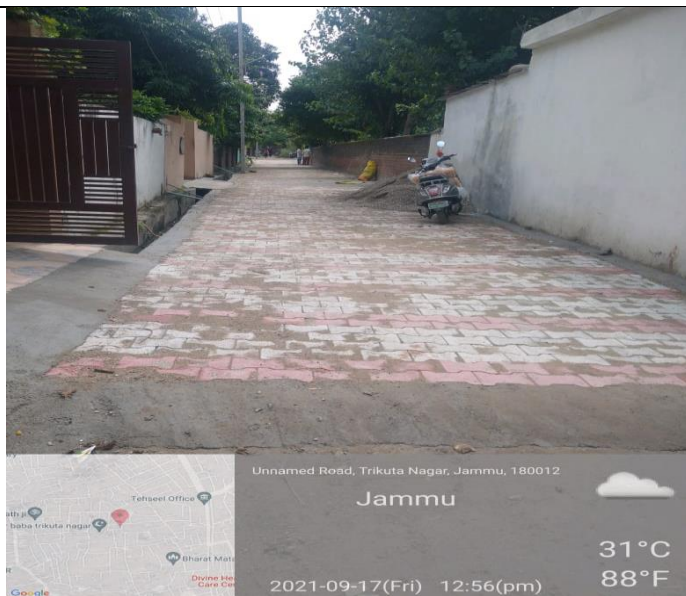

Sr.no	44
Name of the work with Location	Construction of the tile work in lane from Hno.63P, II extn. Khoo wali Gali Vijay Sharma in ward no.53
Department/Organization	JMC
Executive Agency	JMC
Block /District	JAMMU
AA Cost (Rs in Lakhs)	2.67
Total Cost of Completion/Expenditure Incurred ending 3/2022	1.55
Date of Start Month/Year	1-3-2022
Date of Completion	17-3-2022
No of Beneficiaries	500




Sr.no	45
Name of the work with Location	Upgradation of rain from H/o.41,42,43,44-P Sec-6 and near SBI Bank sector-5A , Trikuta Nagar ward no.54
Department/Organization	JMC
Executive Agency	JMC
Block /District	JAMMU
AA Cost (Rs in Lakhs)	2.67
Total Cost of Completion/Expenditure Incurred ending 3/2022	1.62
Date of Start Month/Year	9-8-2021
Date of Completion	7-9-2021
No of Beneficiaries	160





Sr.no	46
Name of the work with Location	Upgradation of lane providing & fixing of interlock tiles in kashmiri Mohalla (Pandit) Gangyal at ward no.56
Department/Organization	JMC
Executive Agency	JMC
Block /District	JAMMU
AA Cost (Rs in Lakhs)	2.67
Total Cost of Completion/Expenditure Incurred ending 3/2022	1.58
Date of Start Month/Year	16-10-2021
Date of Completion	29-10-2021
No of Beneficiaries	190

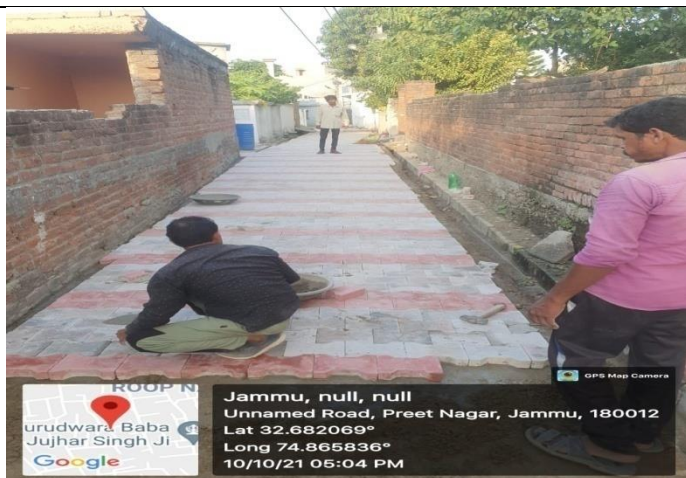

Sr.no	47
Name of the work with Location	Providing and fixing of the interlock tiles in Mohalla Roop-Nagar Gangyal ward no.57 under CCDP Head for the year 21-22
Department/Organization	JMC
Executive Agency	JMC
Block /District	JAMMU
AA Cost (Rs in Lakhs)	2.67
Total Cost of Completion/Expenditure Incurred ending 3/2022	1.72
Date of Start Month/Year	15-10-2021
Date of Completion	15-11-2021
No of Beneficiaries	222



--	--	--



Sr.no	48
Name of the work with Location	Construction of lane by way of interlocked tiles from H/o. Sukhvinder Singh to H/o. L.S.Sokhia Singh links lane no.10 ,98 at ward no.68
Department/Organization	JMC
Executive Agency	JMC
Block /District	JAMMU
AA Cost (Rs in Lakhs)	2.67
Total Cost of Completion/Expenditure Incurred ending 3/2022	1.52
Date of Start Month/Year	21-9-2021
Date of Completion	16-3-2022
No of Beneficiaries	250



Sr.no	49
Name of the work with Location	Construction of the drain near Stadium sector-G in ward no.69 Sainik Colony under CCDP Head for the year 21-22.
Department/Organization	JMC
Executive Agency	JMC
Block /District	JAMMU
AA Cost (Rs in Lakhs)	2.67
Total Cost of Completion/Expenditure Incurred ending 3/2022	1.57
Date of Start Month/Year	16-10-2021

	Date of Completion	12-11-2021
	No of Beneficiaries	350





Sr.no	50
Name of the work with Location	Construction of drain at sector -D from Hno.78 Sainik Colony ward no.70 (near little flower school)
Department/Organization	JMC
Executive Agency	JMC
Block /District	JAMMU
AA Cost (Rs in Lakhs)	2.67
Total Cost of Completion/Expenditure Incurred ending 3/2022	1.56
Date of Start Month/Year	7-12-2021
Date of Completion	5-3-2022
No of Beneficiaries	450



Sr.no	51
Name of the work with Location	Construction/ Upgradation of drain near Gurudwara lower Gadigarh ward no.73
Department/Organization	JMC
Executive Agency	JMC
Block /District	JAMMU
AA Cost (Rs in Lakhs)	2.67
Total Cost of Completion/Expenditure Incurred ending 3/2022	1.80
Date of Start Month/Year	3-9-2021

	Date of Completion	22-10-2021
	No of Beneficiaries	490

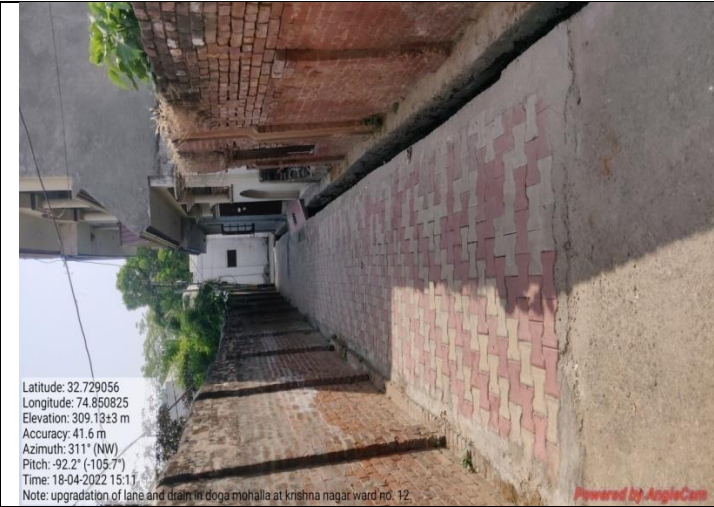 <p>Latitude: 32.729056 Longitude: 74.850825 Elevation: 309.13±3 m Accuracy: 41.6 m Azimuth: 311° (NW) Pitch: -92.2° (-105.7°) Time: 18-04-2022 15:11 Note: upgradation of lane and drain in dogra mohalla at krishna nagar ward no. 12</p>	Sr. No.	52
	Name of the work with Location	Upgradation of Lane Drain in Dogra Mohalla Krishna Nagar Ward. No. 12
	Department/Organization	JMC, Jammu
	Executing Agency	
	Block/District	Jammu
	AA Cost (Rs. In Lakhs)	2.60
	Total Cost of Completion/Expenditure incurred ending 3/2022(Rs. In Lakhs)	1.88
	Date of Start (Month/Year)	09-08-2021
	Date of Completion(Month/Year)	15-09-2021
	No. of beneficiaries	

 <p>Latitude: 32.732054 Longitude: 74.856033 Elevation: 331.61±3 m</p>	Sr. No.	53
	Name of the work with Location	Upgradation of Lane and Drain from H/O Mohan Lal to H/O Ashok Kumar Resham Ghar Colony ward No. 13
	Department/Organization	JMC, Jammu
	Executing Agency	
	Block/District	Jammu
	AA Cost (Rs. In Lakhs)	2.60
	Total Cost of Completion/Expenditure incurred ending 3/2022(Rs. In Lakhs)	1.97



	Date of Start (Month/Year)	09-08-2021
	Date of Completion(Month/Year)	01-09-2021
	No. of beneficiaries	



Sr. No.	54
Name of the work with Location	Construction of Lane and Drain from H/O Anil Gupta to H/O Rakesh Gupta in Sector-3 Bhagwati Nagar Ward No. 14
Department/Organization	JMC, Jammu
Executing Agency	M/S Ramesh Kumar
Block/District	Jammu
AA Cost (Rs. In Lakhs)	2.60
Total Cost of Completion/Expenditure incurred ending 3/2022(Rs. In Lakhs)	1.99
Date of Start (Month/Year)	09-08-2021
Date of Completion(Month/Year)	30-08-2021
No. of beneficiaries	



Sr. No.	55
Name of the work with Location	Construction of Lane and Drain from House of R. P Sharma to House of Katoch Ward No. 16
Department/Organization	JMC, Jammu
Executing Agency	
Block/District	Jammu
AA Cost (Rs. In Lakhs)	2.60
Total Cost of Completion/Expenditure incurred ending 3/2022(Rs. In Lakhs)	2.48
Date of Start (Month/Year)	12-11-2021
Date of Completion(Month/Year)	09-02-2021



	No. of beneficiaries	
--	----------------------	--



Sr. No.	56
Name of the work with Location	Upgradation of Lane by way of tiling from House of Ram Murti to House of Mohinder Pal including side lane.
Department/Organization	JMC
Executing Agency	Ramneek Jamwal
Block/District	Jammu
AA Cost (Rs. In Lakhs)	2.60
Total Cost of Completion/Expenditure incurred ending 3/2022(Rs. In Lakhs)	1.52
Date of Start (Month/Year)	18-10-2021
Date of Completion(Month/Year)	22-12-21



Sr. No.	57
Name of the work with Location	Construction/Up-gradation of Drain and Slab on road along H. No. 53, 54, 64 in Ward No. 22
Department/Organization	JMC, Jammu
Executing Agency	M/S Sunil Bali
Block/District	Jammu
AA Cost (Rs. In Lakhs)	2.60
Total Cost of Completion/Expenditure incurred ending 3/2022(Rs. In Lakhs)	1.96
Date of Start (Month/Year)	23-08-2021
Date of Completion(Month/Year)	22-09-2021
No. of beneficiaries	300





Sr. No.	58
Name of the work with Location	Upgradation of Lane from Sham Tailor Shop to H. No. 121 by way of P/L Tiles Ward No. 23
Department/Organization	JMC, Jammu
Executing Agency	M/S Sunil Bali
Block/District	Jammu
AA Cost (Rs. In Lakhs)	2.60
Total Cost of Completion/Expenditure incurred ending 3/2022(Rs. In Lakhs)	1.87
Date of Start (Month/Year)	10-08-2021
Date of Completion(Month/Year)	20-02-2022
No. of beneficiaries	250



Sr. No.	59
Name of the work with Location	Upgradation of Lane and Drain from H. No. 41 to 45 near Heritage Apartment and from H/O Surjeet Gupta to H/O Shanti Ward No. 24
Department/Organization	JMC, Jammu
Executing Agency	
Block/District	Jammu
AA Cost (Rs. In Lakhs)	2.60
Total Cost of Completion/Expenditure incurred ending 3/2022(Rs. In Lakhs)	1.62


	Date of Start (Month/Year)	31-08-2021
	Date of Completion(Month/Year)	01-10-2021
	No. of beneficiaries	


 <p><b>Karunesh Sharma</b> W-25 GPS Map Camera</p> <p>Jammu, null, null PRWX+MWC, Rehari Colony, Jammu, 180005 Lat 32.74686° Long 74.84955° 18/04/22 11:33 AM</p>	Sr. No.	60
	Name of the work with Location	Upgradation of lane and drain from House of Manu Jamwal
	Department/Organization	JMC
	Executing Agency	Karunesh Sharma
	Block/District	
	AA Cost (Rs. In Lakhs)	2.60
	Total Cost of Completion/Expenditure incurred ending 3/2022(Rs. In Lakhs)	2.10
	Date of Start (Month/Year)	06-12-21
	Date of Completion(Month/Year)	23-12-21
	No. of beneficiaries	80

	Sr. No.	61
	Name of the work with Location	Construction of Lane from H/o Balbir Upto H/o Satpal and H/o Ashwani Kumar upto H/o Ratan Lal by way of P/L Interlocking Tiles Ward No. 48
	Department/Organization	JMC, Jammu
	Executing Agency	M/S Chandar Kant
	Block/District	Jammu
	AA Cost (Rs. In Lakhs)	2.60
	Total Cost of Completion/Expenditure incurred ending 3/2022(Rs. In Lakhs)	2.60
	Date of Start (Month/Year)	20-12-2021



	Date of Completion(Month/Year)	03-01-2022
	No. of beneficiaries	300

	Sr. No.	62
	Name of the work with Location	Construction of Lane in Guru Ravi Dass Mohalla Upper Ward No. 49
	Department/Organization	JMC, Jammu
	Executing Agency	
	Block/District	Jammu
	AA Cost (Rs. In Lakhs)	2.60
	Total Cost of Completion/Expenditure incurred ending 3/2022(Rs. In Lakhs)	1.68
	Date of Start (Month/Year)	03-08-2021
	Date of Completion(Month/Year)	12-12-2021
	No. of beneficiaries	

	Sr. No.	63
	Name of the work with Location	Upgradation of Lane and Drain in Sector-1 along the park Ward No. 50
	Department/Organization	JMC, Jammu
	Executing Agency	
	Block/District	Jammu
	AA Cost (Rs. In Lakhs)	2.60
	Total Cost of Completion/Expenditure incurred ending 3/2022(Rs. In Lakhs)	1.53
	Date of Start (Month/Year)	16-08-2021
	Date of Completion(Month/Year)	12-09-2021
	No. of beneficiaries	





Sr. No.	64
Name of the work with Location	Construction of lane near Saudh Mohalla / Brahman Mohalla by way of tilling.
Department/Organization	JMC
Executing Agency	
Block/District	
AA Cost (Rs. In Lakhs)	2.60
Total Cost of Completion/Expenditure incurred ending 3/2022(Rs. In Lakhs)	2.38
Date of Start (Month/Year)	2-09-2021
Date of Completion(Month/Year)	30-09-2021
No. of beneficiaries	
