
	Name of the work with location.	Sr.No. 1 Black topping of lanes back side of Arya SamajMandir and along AaryaSamaj Park in Ward No: 28 Bakshi Nagar Jammu
	Department/Organization	JMC Div-II
	Executing Agency	JMC
	Block/District	Jammu
	AA cost (Rs: in Lacs)	5.35
	Total Expdt incurred ending 3/2022	5.31
	Date of start (MM/YY)	18.02.22
	Date of Completion (MM/YY)	08.03.22
	No of beneficiaries	

	Name of the work with location.	Sr.No:2: premixing of lane No: 17 (Guru Ravi Das ji Temple) and lane No: 29, Rajpura
	Department/Organization	JMC Div-II
	Executing Agency	JMC
	Block/District	Jammu
	AA cost (Rs: in Lacs)	7.10
	Total Expdt incurred ending 3/2022	5.24
	Date of start (MM/YY)	10.11.21
	Date of Completion (MM/YY)	02.07.22
	No of beneficiaries	



Name of the work with location.	Sr.No: 3 Premixing of lane No: 1, 2, 8 and 9 of Shakti Nagar Ward No: 29
Department/Organization	JMC Div-II
Executing Agency	JMC
Block/District	Jammu
AA cost (Rs: in Lacs)	11.44
Total Expdt incurred ending 3/2022	10.57
Date of start (MM/YY)	07.11.21
Date of Completion (MM/YY)	03.03.22
No of beneficiaries	



Name of the work with location.

Sr.No:4
 Rep/Remodeling of lane from shop of KrishanPansariUpto H/o Ashok Kumar Anmol General Store Lane No: 10, from H/o BattanMaisi to H/o Manga Ram near Nallah and L.No: 4, Repair/Remodelling of lane from Subash Milk Shop to H/o Gurnam Singh, Repair/remodeling of lane from H/o Sansormistri to H/o Rajesh Gupta and lane from near transformer along R/s of Nalalh Shakti Nagar, Upgradation/constt of lane from bbackside of AmbedkarChowk to Backside of Rajpura Park near transformer, Repair/remodeling of lane no: 8 opp. KrishanPansari Shop Rajpura from Chowk to Sat Ashram

Department/Organization	JMC Div-II
Executing Agency	JMC
Block/District	Jammu
AA cost (Rs: in Lacs)	35.00
Total Expdt incurred ending 3/2022	21.46
Date of start (MM/YY)	08.02.22
Date of Completion (MM/YY)	20.03.22
No of beneficiaries	



Name of the work with location.

Sr.No:5
Upgd of L/D from H/o Ram Lal Saini /Ambe Transformer upto H/o Chajju Singh ShantNagar , Lane Opp. Swarna Niwas 3/115 Indira Viharupto H/No. 104 Ram vihar, lane from Doctor Clinic upto H/o KarilalooHNo. 2/106 Ram Vihar, L/D From Shop of Sham PansariuptoSubashChanderShant nagar, From H/o Sh. Ram das upto Om Parkash ,From H/o Sh. Sukesh Thakur HNo. 176/B upto H/o Tara Chand HNo. 265-C ram Vihar ,Imp/ Ren. of L/D Khanna Lane Opp. Bread factory Pandoka Colony D/E for Upgd of lane by way of Paver tiles and Reconst. drains along the lane from the h/o RajnikoulHNo 62 upto h/oPuran Singh

Department/Organization	JMC Div-II
Executing Agency	JMC
Block/District	Jammu
AA cost (Rs: in Lacs)	35.00
Total Expdt incurred ending 3/2022	20.73
Date of start (MM/YY)	30.01.22
Date of Completion (MM/YY)	22.03.22
No of beneficiaries	



Name of the work with location.

Sr.No:6
D/E for Upgradation of lane, From Vikas General Store to Luthra House and , Lane opp Mahajan Enterprises at Janipur ward No. 37, Lane from Raj kumarKhajuriaupto H/o Satish Sharma at Janipur colony Ward no. 3, lane back side H/o advocate Sh. Sandeep Gupta at Janipur Ward no. 37, Lane around Park Major Ajay Singh Jasrotia and veer Savar Bar Park ward No. 37, Lane from H/o DalipGambel to H/o Subhdev Raina near Shiv Mandir Janipur ward No. 37

Department/Organization

JMC Div-II

Executing Agency

JMC

Block/District

Jammu

AA cost (Rs: in Lacs)

35.00

Total Expdt incurred ending 3/2022

20.90

Date of start (MM/YY)

18.01.22

Date of Completion (MM/YY)

24.02.22

No of beneficiaries




Name of the work with location.

Sr.No:7
Upgd/Const/ of lane from H/O Janak Raj to Rajinder Kumar in Vikas Nagar adjoining Gupta Traders, Upgradation of lane by W/o laying from H/o Gurdas to Om Prakash and Neelam Colony, Upgd of lane paver tiles at Shanti Nagar, Upgd/Const. of lane from H/o Kewalkrishan to H/o Dian Chand and adjoining lane in ThtharPatoli, Reconstt. of lane from H/o Baljeet Singh to H/o Hera Singh and H/o Kuldeep Kamal to H/o Ravinder, Upgd/constt. of lane from main road to H/o S.K Bhan at Shakti Nagar, Upgd of lane from H/o Rattan pal to H/o Rajinder Singh and surinder Singh to Puran Singh MairaMohallaTophSherkhnaiyan Ward No: 39

Department/Organization	JMC Div-II
Executing Agency	JMC
Block/District	Jammu
AA cost (Rs: in Lacs)	35.00
Total Expdt incurred ending 3/2022	21.37
Date of start (MM/YY)	20.01.22
Date of Completion (MM/YY)	10.03.22
No of beneficiaries	




Name of the work with location.	Sr.No:8 Black topping of lanes from (a) H/o Sh. S.S Arroara upto Shani Temple Qasim Nagar Ward No: 28 Bakshi Nagar.(b) from Shani temple upto Gupta General Store Gurha Bakshi Nagar in Ward no; 28
Department/Organization	JMC Div-II
Executing Agency	JMC
Block/District	Jammu
AA cost (Rs: in Lacs)	2.90
Total Expdt incurred ending 3/2022	2.89
Date of start (MM/YY)	11/21
Date of Completion (MM/YY)	12/21
No of beneficiaries	

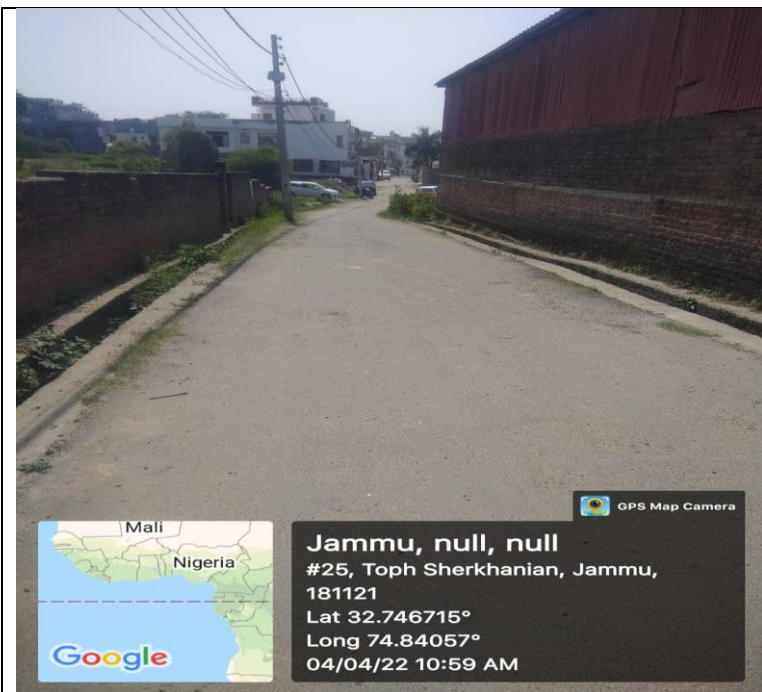


Name of the work with location.	Sr.No:9 Premixing of road from Glove factory to H/o Sher Singh TophSherkhnaiyan Ward No: 39
Department/Organization	JMC Div-II
Executing Agency	JMC
Block/District	Jammu
AA cost (Rs: in Lacs)	3.16
Total Expdt incurred ending 3/2022	2.35
Date of start (MM/YY)	11/21
Date of Completion (MM/YY)	12/21
No of beneficiaries	



Name of the work with location.	Sr.No:10 Premixing of lane at ShardaBhawaniMandirPouniChak, Primary School PouniChak at H/o Sh. PanditaSantraMorh Lane at BabitaSarpanch in Ward No: 32
Department/Organization	JMC Div-II
Executing Agency	JMC
Block/District	Jammu
AA cost (Rs: in Lacs)	8.46
Total Expdt incurred ending 3/2022	5.54
Date of start (MM/YY)	03.03.22
Date of Completion (MM/YY)	3/22
No of beneficiaries	

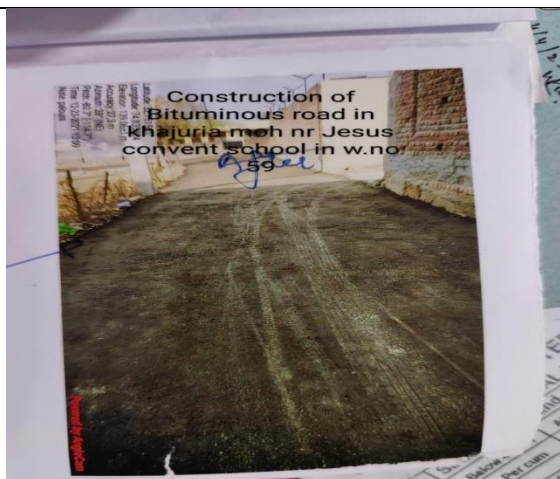

Sr. No.	11
Name of the work with Location	(i) Construction of Bituminous road in Khajuria Mohalla near Jesus Convent School & Link Road W. NO. 59
Department/Organisation	H&UDD
Executive Agency	JAMMU MUNICIPAL CORPORATION DIVISION NO. IIII
Block/District	JAMMU
AA Cost (Rs . in Lakhs)	9.71
Total Cost of Completion/expenditure incurred ending 3/2022	8.29
Date of Start(Month/Year)	01-12-2021
Date of Completion (Month / Year)	22-12-2021
No. of beneficiaries	500

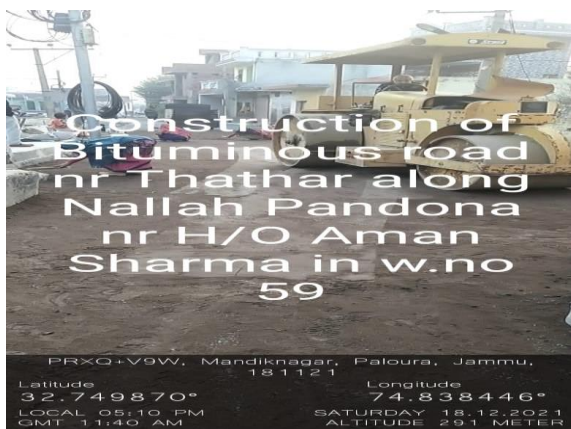

Sr. No.	12
Name of the work with Location	(ii) Construction / Upgradation of Bituminous road near Thathar along Nallah Pandona Near H/o Aman Sharma W.NO. 59
Department/Organisation	H&UDD
Executive Agency	JAMMU MUNICIPAL CORPORATION DIVISION NO. III
Block/District	JAMMU
AA Cost (Rs . in Lakhs)	19.58
Total Cost of Completion/expenditure incurred ending 3/2022	18.98
Date of Start(Month/Year)	01-12-2021
Date of Completion (Month / Year)	02-01-2022
No. of beneficiaries	700

***up grad of road Jmc
road in w no 63***



Sr. No.	13
Name of the work with Location	Upgradation of lane b/w of laying premix carpet lane no. 6,5,4,1 near carpenter office kamal nagar Sector – II near Govt. School to H/o Banam Singh to Mh. Gulam in W.No. 63
Department/Organisation	H&UDD
Executive Agency	JAMMU MUNICIPAL CORPORATION DIVISION NO. III
Block/District	JAMMU
AA Cost (Rs . in Lakhs)	32.80
Total Cost of Completion/expenditure incurred ending 3/2022	31.15
Date of Start(Month/Year)	20-02-2022
Date of Completion (Month / Year)	29-03-2022
No. of beneficiaries	850

**up grad of lane drain
lower upper thather k v
nagar bantalab in w no
63**



Sr. No.	14
Name of the work with Location	Construction of Lane / Drain at near Peepal Tree / Near Puran Singh at Keran and Lane at Lower Thather Near H/o Puran Singh / H/o Jay Singh / H/o Ashok Kuymar / H/o Harbans Lal and near Bharwali Chapri, Upgradation of lane at Bhagat Mohalla UpperThather and Lane Drain from H/o Subash Verma to Suraj Verma at Thather, Upgradation of lane at KV Nagar / Thather / Keran Bantalab W. NO. 63
Department/Organisation	H&UDD
Executive Agency	JAMMU MUNICIPAL CORPORATION DIVISION NO. III
Block/District	JAMMU
AA Cost (Rs . in Lakhs)	34.50
Total Cost of Completion/expenditure incurred ending 3/2022	18.87
Date of Start(Month/Year)	20-01-2022
Date of Completion (Month / Year)	20-03-2022
No. of beneficiaries	600

**up grad of lane drain
shazadpur ganguwan
in w no 72**




Sr. No.	15
Name of the work with Location	Const of lane from H/o Prem Singh to h/o Mangal Singh and allied links at Mohalla , L/D from H/o Parveen Singh to Main Road and drains from Shankar Singh to Mangal Singh at Gangwan Shehzadpur, Lane from Parveen Kumar House to Raj Kumar House and Ram Pal to Hans Raj house and drain from h/o Hem Raj to virshi house, Const of lane from Balwan Singh House to Main Road Shehzadpur and allied links to house of Amar Nath and Gattu Ram, L/D from H/o Sanga Ram to Main Road Patyalichak., L/D from H/o Mohan Lal to Tikri Road, L/D main road Darian to house of Des Raj PatyaliChak. W.NO. 72
Department/Organisation	H&UDD
Executive Agency	JAMMU MUNICIPAL CORPORATION DIVISION NO. III
Block/District	JAMMU
AA Cost (Rs . in Lakhs)	34.50
Total Cost of Completion/expenditure incurred ending 3/2022	25.60
Date of Start(Month/Year)	25-01-2022
Date of Completion (Month / Year)	10-03-2022
No. of beneficiaries	600



Sr.no	16
Name of the work with Location	Macadamization of Road by w/o premixing at internal roads of sec-5 A Trikuta Palace sec- 5,6,7,8 and 9 in Trikuta Nagar in ward no 54
Department/Organization	JMC
Executive Agency	JMC
Block /District	JAMMU
AA Cost (Rs in Lakhs)	23.50
Total Cost of Completion/Expenditure Incurred ending 3/2022	18.23
Date of Start Month/Year	1-3-2022
Date of Completion	14-3-2022
No of Beneficiaries	385



Sr.no	17
Name of the work with Location	Macadamization of Roads by w/o premixing at Internal roads of Green Avenue Model Town, Akali kour Singh Jeevan Nagar Ward no 58.
Department/Organization	JMC
Executive Agency	JMC
Block /District	JAMMU
AA Cost (Rs in Lakhs)	33.00
Total Cost of Completion/Expenditure Incurred ending 3/2022	30.75
Date of Start Month/Year	5-11-2021
Date of Completion	26-3-2022
No of Beneficiaries	300

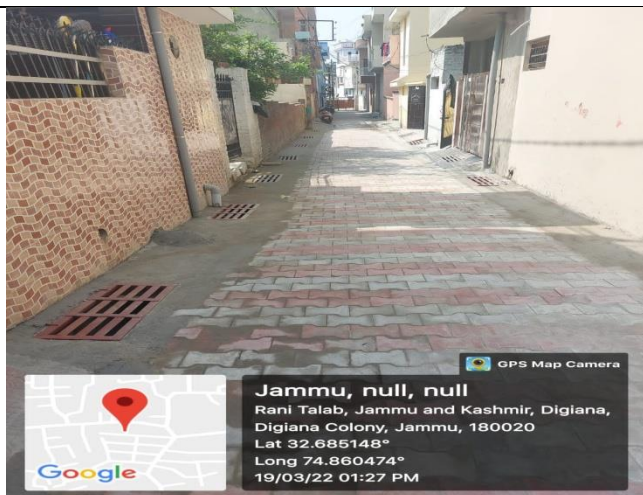

Sr.no	18
Name of the work with Location	Constt. of lane and rain from shakti tent house to Sardari Lal h no 626 Digiana ward no 45, Repair/covering of drain at various locations in Digiana and preet nagar ward no 45, Constt. of lane no 1 from H/o Milki Ram to Janak sehni house digiana and vijay kumar to H/o Megh nath Gupta preet nagar near Ravi Dass temple ward no 45
Department/Organization	JMC
Executive Agency	JMC
Block /District	JAMMU
AA Cost (Rs in Lakhs)	34.50
Total Cost of Completion/Expenditure Incurred ending 3/2022	20.83
Date of Start Month/Year	3-2-2022
Date of Completion	16-3-2022
No of Beneficiaries	700



Sr.no	19
Name of the work with Location	Upgradation of lane by way of paver tiles from H/o. Rugavir singh Jamwal to onwards in ward no.52, Upgradation of lane by way of paver tiles near Hno.303 sector Trikuta Nagar (South extn.)ixing of gratings & slabs near H/o. Jadhish kumar & Balvinder singh (South extn.), Upgradation of lane by way of paver tiles near lane no.1/A opp. Tube well near Harvinder Public School., Upgradation of lane by paver tiles in east extn. Marble lane IV ward no.52
Department/Organization	JMC
Executive Agency	JMC
Block /District	JAMMU
AA Cost (Rs in Lakhs)	34.50
Total Cost of Completion/Expenditure Incurred ending 3/2022	15.13
Date of Start Month/Year	12-3-2022
Date of Completion	17-3-2022
No of Beneficiaries	500



Sr. No.	20
Name of the work with Location	Providing and laying of 2.5 open graded premix carpet on various internal roads of ward No.13.
Department/Organization	JMC
Executing Agency	JMC Div. V
Block/District	Jammu
AA Cost (Rs. In Lakhs)	29.7
Total Cost of Completion/Expenditure incurred ending 3/2022(Rs. In Lakhs)	29.5
Date of Start (Month/Year)	30-11-2021
Date of Completion(Month/Year)	11-01-2022
No. of beneficiaries	300



Sr. No.	21
Name of the work with Location	Providing and laying of 2.5 open graded premix carpet on various internal roads of ward No.14.
Department/Organization	JMC
Executing Agency	
Block/District	
AA Cost (Rs. In Lakhs)	28.82
Total Cost of Completion/Expenditure incurred ending 3/2022(Rs. In Lakhs)	24.25
Date of Start (Month/Year)	05-11-2021
Date of Completion(Month/Year)	18-12-2021
No. of beneficiaries	350

