





Name of the work with location.	S.No. 1 Construction/improvement of park of Ram Talai Mandir, Jullaka Mohalla
Department/Organization	H&UDD
Executing Agency	Jammu Municipal Corporation
Block/District	Jammu
Estimated Cost	7.12
Total Expdt incurred ending 3/2022	7.10
Project Initiation Year	2021
Date of Completion (MM/YY)	10.02.2022
No of beneficiaries	

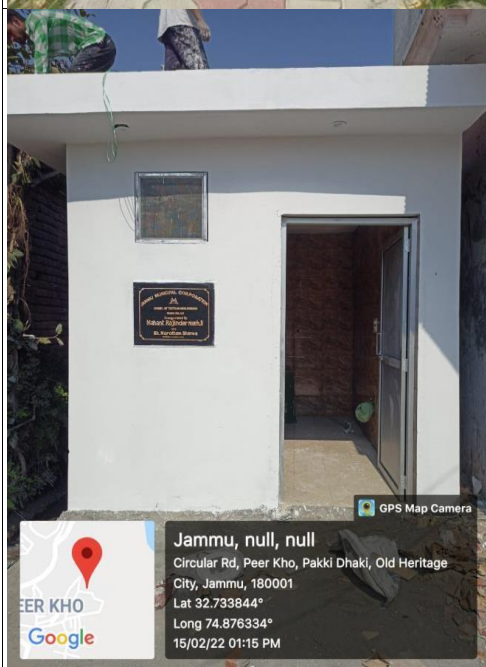


Name of the work with location.	S.No. 2 Const. of Turtian near Peerkho
Department/Organization	H&UDD
Executing Agency	Jammu Municipal Corporation
Block/District	Jammu
Estimated Cost	5.69
Total Expdt incurred ending 3/2022	4.05
Project Initiation Year	2021
Date of Completion (MM/YY)	02.02.2022
No of beneficiaries	

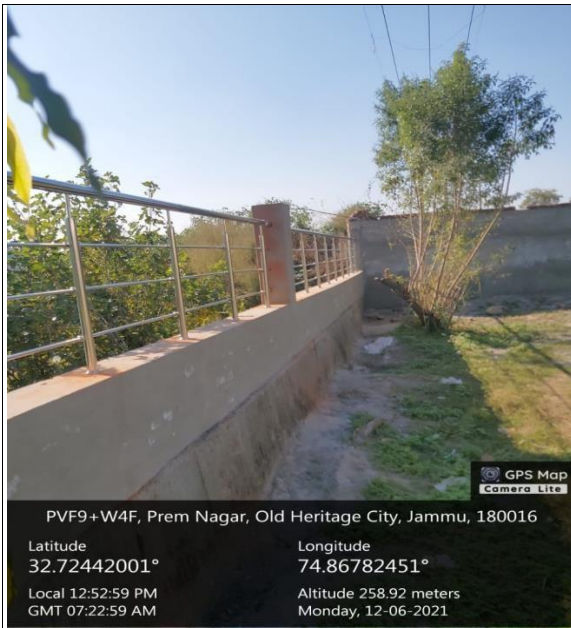


Name of the work with location.	S.No. 3 a)Construction/Improvement of Park near Dakshwari TemplePeerkho
Department/Organization	H&UDD
Executing Agency	Jammu Municipal Corporation
Block/District	Jammu
Estimated Cost	2.66
Total Expdt incurred ending 3/2022	2.65
Project Initiation Year	2021
Date of Completion (MM/YY)	20.10.2021
No of beneficiaries	



Name of the work with location.	S.No. 4 Improvement/Up-gradation of Graveyards
Department/Organization	H&UDD
Executing Agency	Jammu Municipal Corporation
Block/District	Jammu
Estimated Cost	5.43
Total Expdt incurred ending 3/2022	5.42
Project Initiation Year	2021
Date of Completion (MM/YY)	12.12.2021
No of beneficiaries	

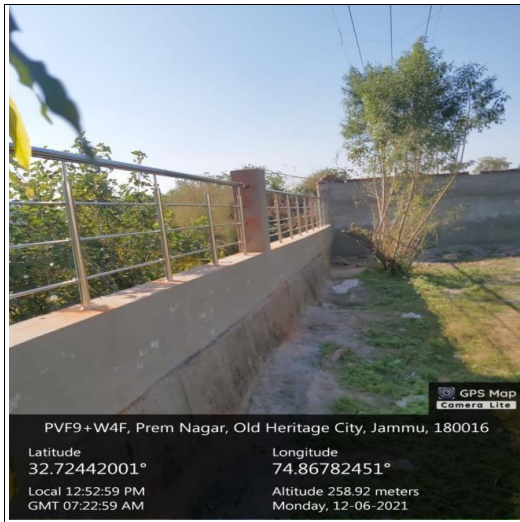







Name of the work with location.	S.No. 5 Improvement / Upgradation of existing park at Jogi Gate, cremation ground
Department/Organization	H&UDD
Executing Agency	Jammu Municipal Corporation
Block/District	Jammu
Estimated Cost	9.90
Total Expdt incurred ending 3/2022	9.89
Project Initiation Year	2021
Date of Completion (MM/YY)	15.01.2022
No of beneficiaries	

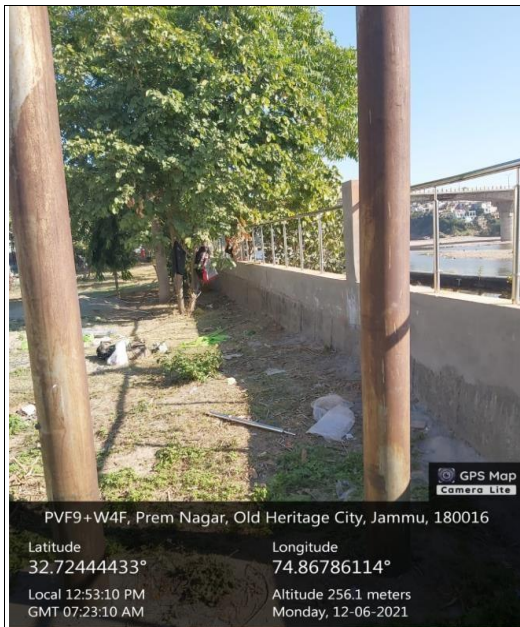

Name of the work with location.	S.No. 6 Upgradation of Purani Mandi Park
Department/Organization	H&UDD
Executing Agency	Jammu Municipal Corporation
Block/District	Jammu
Estimated Cost	7.14
Total Expdt incurred ending 3/2022	7.11
Project Initiation Year	2021
Date of Completion (MM/YY)	15.12.2021
No of beneficiaries	




 	Name of the work with location.	S.No. 7 Improvement of Bathing Ghat /Tuttian at Shree Radha Krishan Temple
	Department/Organization	H&UDD
	Executing Agency	Jammu Municipal Corporation
	Block/District	Jammu
	Estimated Cost	5.69
	Total Expdt incurred ending 3/2022	5.67
	Project Initiation Year	2021
	Date of Completion (MM/YY)	09.11.2021
 	No of beneficiaries	
	Name of the work with location.	S.No. 8 Construction/Improvement of Community Hall at Geeta Bhawan , Parade
	Department/Organization	H&UDD
	Executing Agency	Jammu Municipal Corporation
	Block/District	Jammu
	Estimated Cost	23.37
	Total Expdt incurred ending 3/2021	17.50
	Project Initiation Year	2021
 	Date of Completion (MM/YY)	05.03.2022
	No of beneficiaries	



Name of the work with location.	S.No. 9 Upgradation of Children Graveyard by way of Construction of paths, repair to boundary wall etc. at QasimNagar
Department/Organization	H&UDD
Executing Agency	Jammu Municipal Corporation
Block/District	Jammu
Estimated Cost	5.35
Total Expdt incurred ending 3/2022	5.35
Project Initiation Year	2021
Date of Completion (MM/YY)	22.11.2021
No of beneficiaries	



Name of the work with location.	S.No. 10 Renovation of existing Tuttian at KachaTalab Bahufort
Department/Organization	H&UDD
Executing Agency	Jammu Municipal Corporation
Block/District	Jammu
Estimated Cost	3.00
Total Expdt incurred ending 3/2022	2.28
Project Initiation Year	2021
Date of Completion (MM/YY)	16.10.2021
No of beneficiaries	

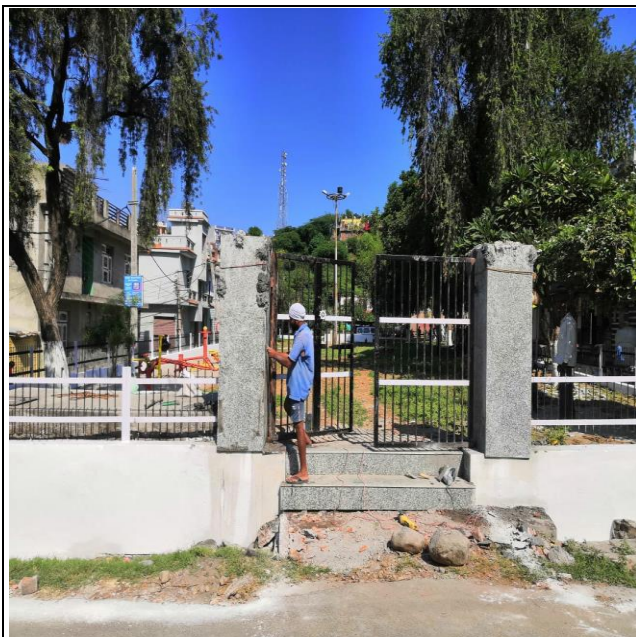



Name of the work with location.	S.No. 11 Renovation of JMC park at New Bahu fort Colony
Department/Organization	H&UDD
Executing Agency	Jammu Municipal Corporation
Block/District	Jammu
Estimated Cost	5.00
Total Expdt incurred ending 3/2022	3.31
Project Initiation Year	2021
Date of Completion (MM/YY)	16.10.2021
No of beneficiaries	





Name of the work with location.	S.No. 12 Construction of Bathing Ghat / Tuttian Near Govt. Middle School Majeen
Department/Organization	H&UDD
Executing Agency	Jammu Municipal Corporation
Block/District	Jammu
Estimated Cost	8.00
Total Expdt incurred ending 3/2021	5.57
Project Initiation Year	2021
Date of Completion (MM/YY)	10.01.2022
No of beneficiaries	
Name of the work with location.	UPGRADATION OF GRAVEYARD LOWER RANGOORA




	Name of the work with location.	S.No 13 UPGRADATION OF GRAVEYARD LOWER RANGOORA W.NO 71
	Department/Organization	H&UDD
	Executing Agency	Jammu Municipal Corporation
	Block/District	Jammu
	Estimated Cost	8.00
	Total Expdt incurred ending 3/2022	7.86
	Project Initiation Year	2021
	Date of Completion (MM/YY)	18.02.2022
	No of beneficiaries	


	Name of the work with location.	S.No 14 UPGRADATION OF PARK AT CHOWGAN SALATHIA MUBARAK MANDI W.NO 1
	Department/Organization	H&UDD
	Executing Agency	Jammu Municipal Corporation
	Block/District	Jammu
	Estimated Cost	3.20
	Total Expdt incurred ending 3/2022	2.20
	Project Initiation Year	2021
	Date of Completion (MM/YY)	25.03.2022
	No of beneficiaries	


	Name of the work with location.	S.No. 15 Repair/Renovation of Tuttian near PHE Sub-Division
	Department/Organization	JMC Div-II
	Executing Agency	JMC
	Block/District	Jammu
	AA cost (Rs: in Lacs)	5.00
	Total Expdt incurred ending 3/2022	3.86
	Date of start (MM/YY)	14.12.21
	Date of Completion (MM/YY)	30.01.22
	No of beneficiaries	

	Name of the work with location.	S.No. 16 Const./Development of ShishuSamadhian opp. Police Station
	Department/Organization	JMC Div-II
	Executing Agency	JMC
	Block/District	Jammu
	AA cost (Rs: in Lacs)	20.00
	Total Expdt incurred ending 3/2022	14.20
	Date of start (MM/YY)	19.09.21
	Date of Completion (MM/YY)	15.03.22
	No of beneficiaries	



	Name of the work with location.	S.No. 17 Repair/upgradation of Park at Rajpura Near Dr. B.R Ambedkar School
	Department/Organization	JMC Div-II
	Executing Agency	JMC
	Block/District	Jammu
	AA cost (Rs: in Lacs)	5.00
	Total Expdt incurred ending 3/2022	4.15
	Date of start (MM/YY)	15.10.21
	Date of Completion (MM/YY)	28.11.21
	No of beneficiaries	



	Name of the work with location.	S.No. 18 Development/Const. of parking space at Gurudwara in TalabTillo
	Department/Organization	JMC Div-II
	Executing Agency	JMC
	Block/District	Jammu
	AA cost (Rs: in Lacs)	25.00
	Total Expdt incurred ending 3/2022	14.21
	Date of start (MM/YY)	19.09.21
	Date of Completion (MM/YY)	17.03.22
	No of beneficiaries	

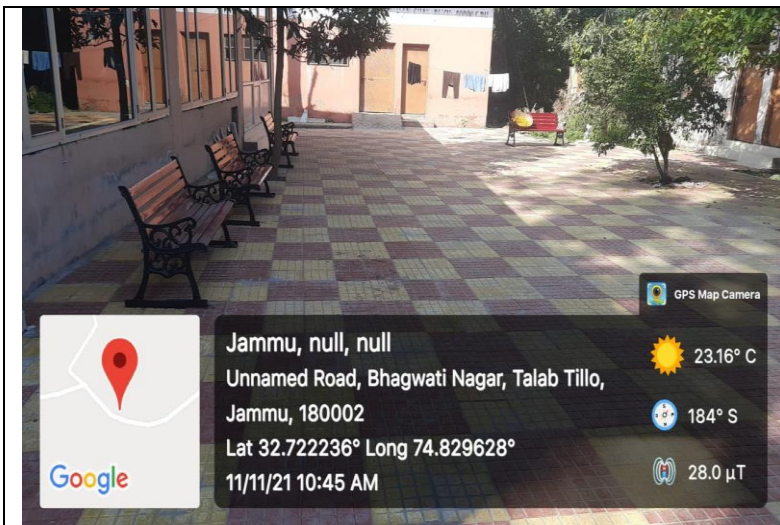



Name of the work with location.	S.No.19 Balance work of community hall at cremation ground Panjpeer
Department/Organization	JMC Div-II
Executing Agency	JMC
Block/District	Jammu
AA cost (Rs: in Lacs)	10.00
Total Expdt incurred ending 3/2022	5.78
Date of start (MM/YY)	10.09.21
Date of Completion (MM/YY)	29.09.21
No of beneficiaries	





Name of the work with location.	S.No. 20 Balance work of community hall at puran baba mandir
Department/Organization	JMC Div-II
Executing Agency	JMC
Block/District	Jammu
AA cost (Rs: in Lacs)	10.00
Total Expdt incurred ending 3/2022	5.68
Date of start (MM/YY)	19.09.21
Date of Completion (MM/YY)	04.11.21
No of beneficiaries	



 <div data-bbox="69 443 232 580">  </div> <div data-bbox="250 448 797 580"> <p><b>Jammu, null, null</b>            Unnamed Road, Bhagwati Nagar, Talab Tillo, Jammu, 180002            Lat 32.722439°            Long 74.829319°            18/04/22 11:40 AM</p> </div>	Name of the work with location.	S.No. 21 Const. of Tuttian including water tank at cremation ground Panjpeer
	Department/Organization	JMC Div-II
	Executing Agency	JMC
	Block/District	Jammu
	AA cost (Rs: in Lacs)	6.00
	Total Expdt incurred ending 3/2022	4.71
	Date of start (MM/YY)	05.12.21
	Date of Completion (MM/YY)	20.01.22
	No of beneficiaries	


 <div data-bbox="69 1109 309 1246">  </div> <div data-bbox="327 1114 761 1246"> <p><b>Jammu, null, null</b>            12, Shakti Nagar Lane, Shakti Nagar,            Lower Shiv Nagar, Jammu, 180001            Lat 32.737235°            Long 74.836296°            18/04/22 12:28 PM</p> </div>	Name of the work with location.	S.No. 22 Const. of KriyaGhat Opp. Women Polytechnic College
	Department/Organization	JMC Div-II
	Executing Agency	JMC
	Block/District	Jammu
	AA cost (Rs: in Lacs)	6.00
	Total Expdt incurred ending 3/2022	5.07
	Date of start (MM/YY)	15.11.21
	Date of Completion (MM/YY)	15.03.22
	No of beneficiaries	




	Name of the work with location.	S.No. 23 Development of park (Bharat Mata park ) on Patoli Janipur Road Ward no; 35.
	Department/Organization	JMC Div-II
	Executing Agency	JMC
	Block/District	Jammu
	AA cost (Rs: in Lacs)	5.00
	Total Expdt incurred ending 3/2022	3.79
	Date of start (MM/YY)	18.12.21
	Date of Completion (MM/YY)	03.03.22
	No of beneficiaries	


	Name of the work with location.	S.No. 24 Const. of Tuttian in shant nagar
	Department/Organization	JMC Div-II
	Executing Agency	JMC
	Block/District	Jammu
	AA cost (Rs: in Lacs)	5.00
	Total Expdt incurred ending 3/2022	3.89
	Date of start (MM/YY)	03.10.21
	Date of Completion (MM/YY)	15.12.21
	No of beneficiaries	


	<table> <tr> <td>Name of the work with location.</td><td>S.No. 25 Upgradation/development of Chohan Park, Buta Nagar Park &amp;lohan Park in Paloura</td></tr> <tr> <td>Department/Organization</td><td>JMC Div-II</td></tr> <tr> <td>Executing Agency</td><td>JMC</td></tr> <tr> <td>Block/District</td><td>Jammu</td></tr> <tr> <td>AA cost (Rs: in Lacs)</td><td>7.12</td></tr> <tr> <td>Total Expdt incurred ending 3/2022</td><td>7.94</td></tr> <tr> <td>Date of start (MM/YY)</td><td>21.01.21</td></tr> <tr> <td>Date of Completion (MM/YY)</td><td>08.02.22</td></tr> <tr> <td></td><td></td></tr> </table>	Name of the work with location.	S.No. 25 Upgradation/development of Chohan Park, Buta Nagar Park &lohan Park in Paloura	Department/Organization	JMC Div-II	Executing Agency	JMC	Block/District	Jammu	AA cost (Rs: in Lacs)	7.12	Total Expdt incurred ending 3/2022	7.94	Date of start (MM/YY)	21.01.21	Date of Completion (MM/YY)	08.02.22		
Name of the work with location.	S.No. 25 Upgradation/development of Chohan Park, Buta Nagar Park &lohan Park in Paloura																		
Department/Organization	JMC Div-II																		
Executing Agency	JMC																		
Block/District	Jammu																		
AA cost (Rs: in Lacs)	7.12																		
Total Expdt incurred ending 3/2022	7.94																		
Date of start (MM/YY)	21.01.21																		
Date of Completion (MM/YY)	08.02.22																		
	<table> <tr> <td>Name of the work with location.</td><td>S.No. 26 Development of parking space near Lohan park in Paloura</td></tr> <tr> <td>Department/Organization</td><td>JMC Div-II</td></tr> <tr> <td>Executing Agency</td><td>JMC</td></tr> <tr> <td>Block/District</td><td>Jammu</td></tr> <tr> <td>AA cost (Rs: in Lacs)</td><td>30.00</td></tr> <tr> <td>Total Expdt incurred ending 3/2022</td><td>21.61</td></tr> <tr> <td>Date of start (MM/YY)</td><td>21.10.21</td></tr> <tr> <td>Date of Completion (MM/YY)</td><td>05.01.22</td></tr> <tr> <td>No of beneficiaries</td><td></td></tr> </table>	Name of the work with location.	S.No. 26 Development of parking space near Lohan park in Paloura	Department/Organization	JMC Div-II	Executing Agency	JMC	Block/District	Jammu	AA cost (Rs: in Lacs)	30.00	Total Expdt incurred ending 3/2022	21.61	Date of start (MM/YY)	21.10.21	Date of Completion (MM/YY)	05.01.22	No of beneficiaries	
Name of the work with location.	S.No. 26 Development of parking space near Lohan park in Paloura																		
Department/Organization	JMC Div-II																		
Executing Agency	JMC																		
Block/District	Jammu																		
AA cost (Rs: in Lacs)	30.00																		
Total Expdt incurred ending 3/2022	21.61																		
Date of start (MM/YY)	21.10.21																		
Date of Completion (MM/YY)	05.01.22																		
No of beneficiaries																			

 <div data-bbox="53 391 712 510"> <p>TOPH. RKHANIA Devi Google</p> <p><b>Jammu, null, null</b> Rehari Road, Subash Nagar, Jammu, 181121 Lat 32.747079° Long 74.841424° 04/04/22 11:08 AM</p> </div>	Name of the work with location.	S.No. 27 Renovation/upgradation of 02 No. Parks
	Department/Organization	JMC Div-II
	Executing Agency	JMC
	Block/District	Jammu
	AA cost (Rs: in Lacs)	12.00
	Total Expdt incurred ending 3/2022	10.66
	Date of start (MM/YY)	16.10.21
	Date of Completion (MM/YY)	05.01.22
	No of beneficiaries	

 <div data-bbox="53 1093 660 1220"> <p>PATO MAGOTRIAN Google</p> <p><b>Jammu, null, null</b> QR2R+WGP, Patoli Magotrian, Mandiknagar, Paloura, Jammu, 181121 Lat 32.751909° Long 74.841557° 17/03/22 11:11 AM</p> </div>	Name of the work with location.	S.No. 28 Renovation of Graveyard and Tutian at PatoliMangotrian
	Department/Organization	JMC Div-II
	Executing Agency	JMC
	Block/District	Jammu
	AA cost (Rs: in Lacs)	9.00
	Total Expdt incurred ending 3/2022	6.14
	Date of start (MM/YY)	15.10.21
	Date of Completion (MM/YY)	19.02.22
	No of beneficiaries	




	Name of the work with location.	S.No. 29 Const. of Turtian at Cremation ground TophSherkhania
	Department/Organization	JMC Div-II
	Executing Agency	JMC
	Block/District	Jammu
	AA cost (Rs: in Lacs)	9.00
	Total Expdt incurred ending 3/2022	6.75
	Date of start (MM/YY)	05.10.21
	Date of Completion (MM/YY)	06.02.22
	No of beneficiaries	


	Name of the work with location.	S.No. 30 Constt. Of Cremation ground & Community Hall in Ward No: 39
	Department/Organization	JMC Div-II
	Executing Agency	JMC
	Block/District	Jammu
	AA cost (Rs: in Lacs)	36.36
	Total Expdt incurred ending 3/2022	18.18
	Date of start (MM/YY)	24.01.22
	Date of Completion (MM/YY)	09.03.22
No of beneficiaries		

	Name of the work with location.	S.No. 31 Const. of Tutian Opp. PHE medical sub-division Shakti Nagar Near A.G Office
	Department/Organization	JMC Div-II
	Executing Agency	JMC
	Block/District	Jammu
	AA cost (Rs: in Lacs)	7.50
	Total Expdt incurred ending 3/2022	4.85
	Date of start (MM/YY)	20.11.21
	Date of Completion (MM/YY)	05.01.22
	No of beneficiaries	

	Name of the work with location.	S.No. 32 Repair of Tutian near peer baba in kabir nagar
	Department/Organization	JMC Div-II
	Executing Agency	JMC
	Block/District	Jammu
	AA cost (Rs: in Lacs)	5.00
	Total Expdt incurred ending 3/2022	3.365
	Date of start (MM/YY)	02.10.21
	Date of Completion (MM/YY)	09.12.21
	No of beneficiaries	

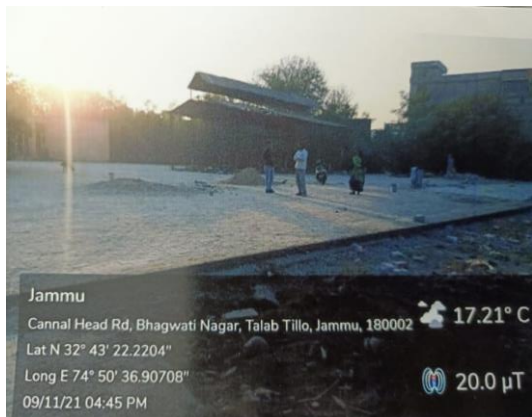


Name of the work with location.	S.No. 33 Balance work of Repair/Renovation of Cremation ground at Durga Nagar
Department/Organization	JMC Div-II
Executing Agency	JMC
Block/District	Jammu
AA cost (Rs: in Lacs)	20.00
Total Expdt incurred ending 3/2022	11.78
Date of start (MM/YY)	01.10.21
Date of Completion (MM/YY)	10.11.21
No of beneficiaries	

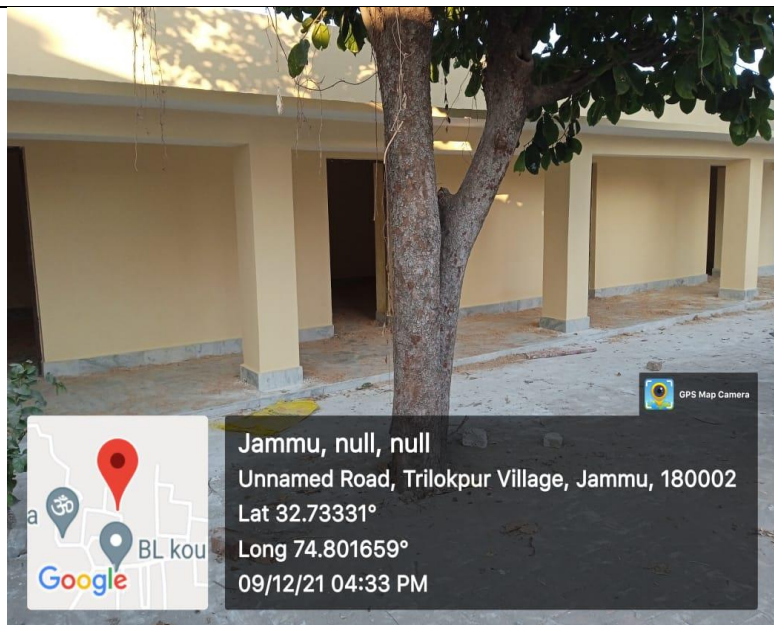

Name of the work with location.	Sr.No:34 Renovation of existing Panchayat Ghar building at Trilokpur
Department/Organization	JMC Div-II
Executing Agency	JMC
Block/District	Jammu
AA cost (Rs: in Lacs)	15.00
Total Expdt incurred ending 3/2022	9.66
Date of start (MM/YY)	02.10.21
Date of Completion (MM/YY)	2511.21
No of beneficiaries	



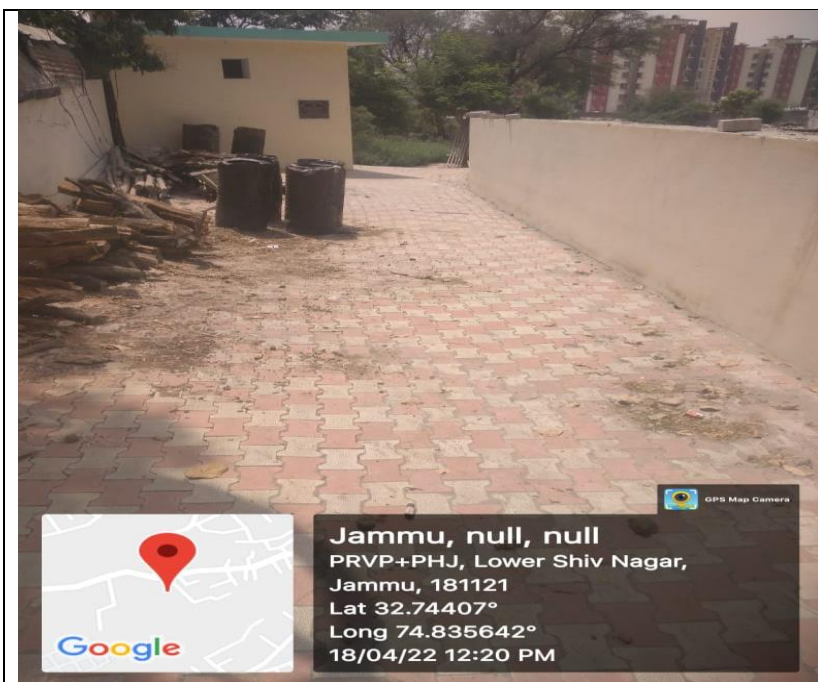


Name of the work with location.	Sr.No:35 Renovation of Graveyard at TophSherkhanian
Department/Organization	JMC Div-II
Executing Agency	JMC
Block/District	Jammu
AA cost (Rs: in Lacs)	12.00
Total Expdt incurred ending 3/2022	7.29
Date of start (MM/YY)	10.11.21
Date of Completion (MM/YY)	01/22
No of beneficiaries	



Name of the work with location.	Sr.No:36 Renovation of Cremation ground TophSherkhanian
Department/Organization	JMC Div-II
Executing Agency	JMC
Block/District	Jammu
AA cost (Rs: in Lacs)	9.00
Total Expdt incurred ending 3/2022	5.31
Date of start (MM/YY)	28.09.21
Date of Completion (MM/YY)	15.11.21
No of beneficiaries	



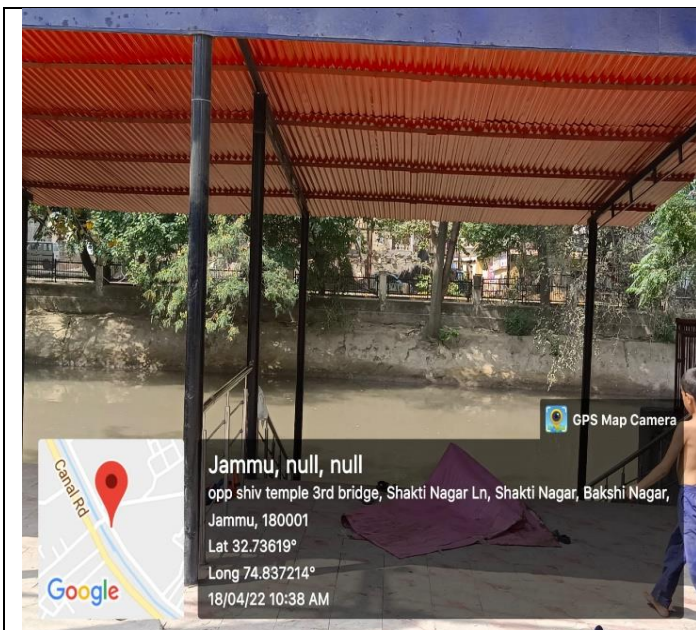

Name of the work with location.	Sr.No:37 Constt. of park in Moga Mohalla Opp. Police Station
Department/Organization	JMC Div-II
Executing Agency	JMC
Block/District	Jammu
AA cost (Rs: in Lacs)	15.00
Total Expdt incurred ending 3/2022	10.10
Date of start (MM/YY)	17.09.21
Date of Completion (MM/YY)	14.11.21
No of beneficiaries	



Name of the work with location.	Sr.No:38 Const. of KriyaGhat opp. PHE medical sub division near A.G office
Department/Organization	JMC Div-II
Executing Agency	JMC
Block/District	Jammu
AA cost (Rs: in Lacs)	7.50
Total Expdt incurred ending 3/2022	5.97
Date of start (MM/YY)	04.10.21
Date of Completion (MM/YY)	06.11.21
No of beneficiaries	




	Name of the work with location.	Sr.No:39 Balance work of community hall at mohallaGujral
	Department/Organization	JMC Div-II
	Executing Agency	JMC
	Block/District	Jammu
	AA cost (Rs: in Lacs)	10.00
	Total Expdt incurred ending 3/2022	5.51
	Date of start (MM/YY)	01.10.21
	Date of Completion (MM/YY)	28.12.21
	No of beneficiaries	

	Name of the work with location.	Sr.No:40 Dvelopment/upgradation of park at Susheel Nagar
	Department/Organization	JMC Div-II
	Executing Agency	JMC
	Block/District	Jammu
	AA cost (Rs: in Lacs)	10.00
	Total Expdt incurred ending 3/2022	6.65
	Date of start (MM/YY)	01.10.21
	Date of Completion (MM/YY)	28.12.21
	No of beneficiaries	



**up grad cremation groud Lower  
upper thather keran k v nagar  
bantalab in w no 63**

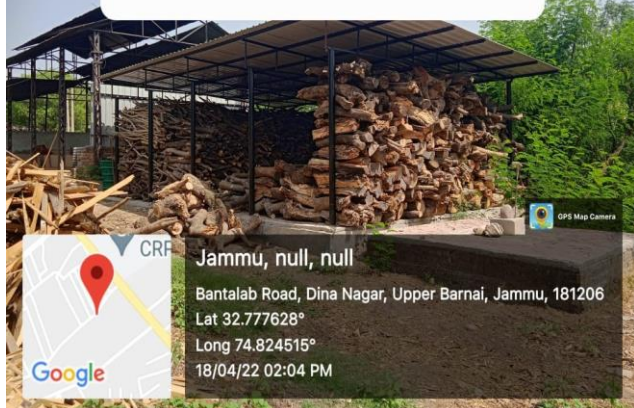

Sr. No.	41,42,43,44
Name of the work with Location	Construction / up gradation of cremation ground upper Thather, Construction /upgradation of Cremation ground upper Keran, Construction /upgradation of Cremation ground lower thather & Construction /upgradation of Cremation ground KB Nagar W.NO.63
Department/Organisation	H&UDD
Executive Agency	JAMMU MUNICIPAL CORPORATION DIVISION NO. III
Block/District	JAMMU
AA Cost (Rs . in Lakhs )	30.00
Total Cost of Completion/expenditure incurred ending 3/2022	19.85
Date of Start(Month/Year)	08-10-2021
Date of Completion ( Month / Year)	05-01-2022
No. of beneficiaries	1250

**up grad of tootiyen bathroom lower  
upper thather keran bantalab in w no  
63**




Sr. No.	45,46
Name of the work with Location	Const. of Tuttur/bathroom at cremation ground upper Keran/lower thather Const. of Tuttur/bathroom at cremation ground upper thather W.NO.63
Department/Organisation	H&UDD
Executive Agency	JAMMU MUNICIPAL CORPORATION DIVISION NO. III
Block/District	JAMMU
AA Cost (Rs . in Lakhs )	20.00
Total Cost of Completion/expenditure incurred ending 3/2022	14.27
Date of Start(Month/Year)	11-10-2021
Date of Completion ( Month / Year)	08-01-2022
No. of beneficiaries	1250

**up grad of cremation  
ground in w no 64**




Sr. No.	47,48
Name of the work with Location	Construction /upgradation of Cremation ground Choudhary Lane & Construction/upgradation of Shishu smadian W.NO. 64
Department/Organisation	H&UDD
Executive Agency	JAMMU MUNICIPAL CORPORATION DIVISION NO. III
Block/District	JAMMU
AA Cost (Rs . in Lakhs )	25.00
Total Cost of Completion/expenditure incurred ending 3/2022	16.13
Date of Start(Month/Year)	05-10-2021
Date of Completion ( Month / Year)	21-02-2022
No. of beneficiaries	1200

**Platform at Cremation  
ground patoli brahmana  
w.no 65**

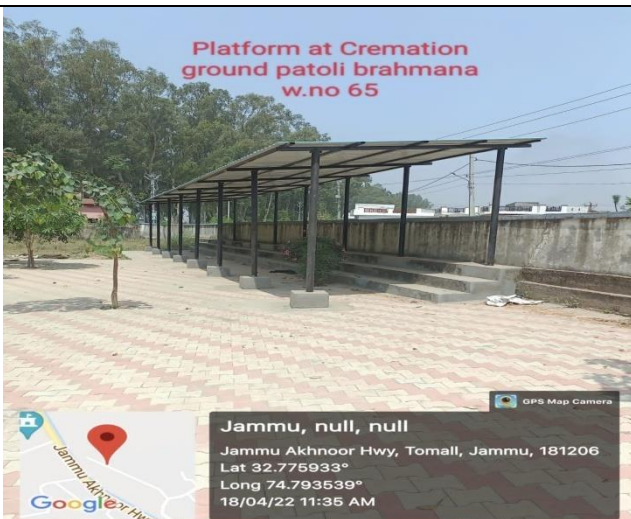

Sr. No.	49
Name of the work with Location	Construction/upgradation of Cremation shed and platform at Patoli Brahmana In W.NO.65
Department/Organisation	H&UDD
Executive Agency	JAMMU MUNICIPAL CORPORATION DIVISION NO. III
Block/District	JAMMU
AA Cost (Rs . in Lakhs )	16.00
Total Cost of Completion/expenditure incurred ending 3/2022	9.69
Date of Start(Month/Year)	05-10-2021
Date of Completion ( Month / Year)	15-02-2022
No. of beneficiaries	950

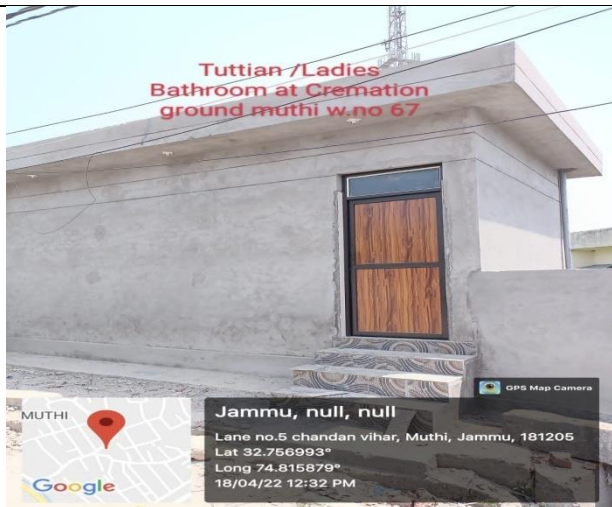

Sr. No.	50
Name of the work with Location	Construction /upgradation of Tuttian/ Ladies bathroom in cremation ground at Muthi IN W.NO.67
Department/Organisation	H&UDD
Executive Agency	JAMMU MUNICIPAL CORPORATION DIVISION NO. III
Block/District	JAMMU
AA Cost (Rs . in Lakhs )	7.50
Total Cost of Completion/expenditure incurred ending 3/2022	5.51
Date of Start(Month/Year)	06-01-2022
Date of Completion ( Month / Year)	03-03-2022
No. of beneficiaries	1200



Sr. No.	51
Name of the work with Location	Construction /upgradation of Kriya ghat at Muthi camp pulley & Muthi Pulleyw.no.67
Department/Organisation	H&UDD
Executive Agency	JAMMU MUNICIPAL CORPORATION DIVISION NO. III
Block/District	JAMMU
AA Cost (Rs . in Lakhs )	21.00
Total Cost of Completion/expenditure incurred ending 3/2022	12.76
Date of Start(Month/Year)	28-10-2021
Date of Completion ( Month / Year)	25-01-2022
No. of beneficiaries	1500





Sr. No.	52
Name of the work with Location	Construction of platform at shishu smadian at Muthi W.NO.67
Department/Organisation	H&UDD
Executive Agency	JAMMU MUNICIPAL CORPORATION DIVISION NO. III
Block/District	JAMMU
AA Cost (Rs . in Lakhs )	10.50
Total Cost of Completion/expenditure incurred ending 3/2022	6.32
Date of Start(Month/Year)	11-10-2021
Date of Completion ( Month / Year)	15-11-2021
No. of beneficiaries	700



Sr. No.	53
Name of the work with Location	Construction/upgradation of park at Baba Kalaikh Nath temple w.no 63
Department/Organisation	H&UDD
Executive Agency	JAMMU MUNICIPAL CORPORATION DIVISION NO. III
Block/District	JAMMU
AA Cost (Rs . in Lakhs )	5.00
Total Cost of Completion/expenditure incurred ending 3/2022	2.99
Date of Start(Month/Year)	10-10-2021
Date of Completion ( Month / Year)	10-12-2021
No. of beneficiaries	1400



Sr. No.	54
Name of the work with Location	Renovation and repair of Mehr Chand Mahajan Park, Mahajan Sabha at Gandhi Nagar in W.No 20
Department/Organisation	H&UDD
Executive Agency	JAMMU MUNICIPAL CORPORATION DIVISION NO. III
Block/District	JAMMU
AA Cost (Rs . in Lakhs )	11.00
Total Cost of Completion/expenditure incurred ending 3/2022	7.55
Date of Start(Month/Year)	19-01-2022
Date of Completion ( Month / Year)	19-02-2022
No. of beneficiaries	600



Sr. No.	55
Name of the work with Location	Construction of cremation shed & path at cremation ground Band Patnyal in W.No 75
Department/Organisation	H&UDD
Executive Agency	JAMMU MUNICIPAL CORPORATION DIVISION NO. III
Block/District	JAMMU
AA Cost (Rs . in Lakhs )	9.80
Total Cost of Completion/expenditure incurred ending 3/2022	6.86
Date of Start(Month/Year)	27-01-2022
Date of Completion ( Month / Year)	27-03-2022
No. of beneficiaries	600





Sr. No.	56
Name of the work with Location	Construction of cremation shed & path at cremation ground Durga Chak in W.No 75
Department/Organisation	H&UDD
Executive Agency	JAMMU MUNICIPAL CORPORATION DIVISION NO. III
Block/District	JAMMU
AA Cost (Rs . in Lakhs )	5.60
Total Cost of Completion/expenditure incurred ending 3/2022	3.99
Date of Start(Month/Year)	26-01-2022
Date of Completion ( Month / Year)	04-03-2022
No. of beneficiaries	500



Sr. No.	57
Name of the work with Location	Construction of boundary wall, Path and other allied works at Graveyard Sangrampur in W.No 75
Department/Organisation	H&UDD
Executive Agency	JAMMU MUNICIPAL CORPORATION DIVISION NO. III
Block/District	JAMMU
AA Cost (Rs . in Lakhs )	9.6
Total Cost of Completion/expenditure incurred ending 3/2022	5.91
Date of Start(Month/Year)	27-01-2022
Date of Completion ( Month / Year)	03-03-2022
No. of beneficiaries	260

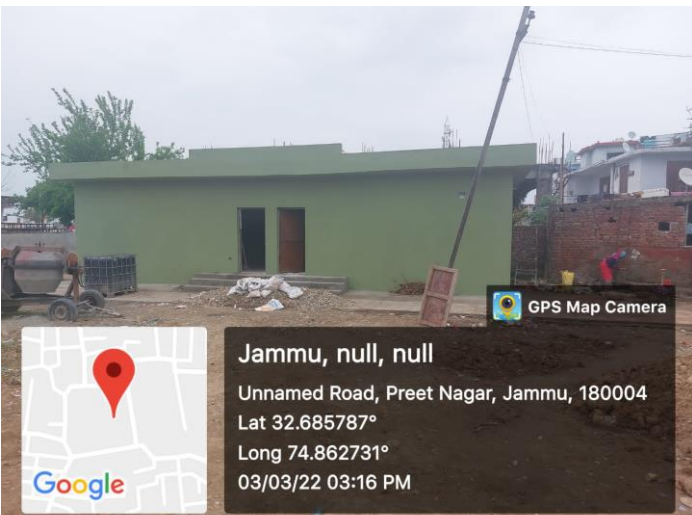

	Sr.no	58
	Name of the work with Location	Constt. of Tutian at sector-4 Rani Talab
	Department/Organization	JMC
	Executive Agency	JMC
	Block /District	JAMMU
	AA Cost (Rs in Lakhs)	15.00
	Total Cost of Completion/Expenditure Incurred ending 3/2022	11.54
	Date of Start Month/Year	25-10-2021
	Date of Completion	15-3-2022
No of Beneficiaries		380

	Sr.no	59
	Name of the work with Location	Landscaping near PHE Tube well Rani Talab
	Department/Organization	JMC
	Executive Agency	JMC
	Block /District	JAMMU
	AA Cost (Rs in Lakhs)	25.00
	Total Cost of Completion/Expenditure Incurred ending 3/2022	14.86
	Date of Start Month/Year	21-11-2021
	Date of Completion	12-3-2022
No of Beneficiaries		290



Sr.no	60
Name of the work with Location	Development of Green space at Babliana road Gangyal
Department/Organization	JMC
Executive Agency	JMC
Block /District	JAMMU
AA Cost (Rs in Lakhs)	12.00
Total Cost of Completion/Expenditure Incurred ending 3/2022	7.31
Date of Start Month/Year	15-11-2021
Date of Completion	25-2-2022
No of Beneficiaries	250



Sr.no	61
Name of the work with Location	Development/Upgradation of Graveyard opp. Digiana Ashram.
Department/Organization	JMC
Executive Agency	JMC
Block /District	JAMMU
AA Cost (Rs in Lakhs)	15.00
Total Cost of Completion/Expenditure Incurred ending 3/2022	10.34
Date of Start Month/Year	11-11-2021
Date of Completion	17-2-2022
No of Beneficiaries	291



Sr.no	62
Name of the work with Location	Development of park No.1-20 in Sainik Colony
Department/Organization	JMC
Executive Agency	JMC
Block /District	JAMMU
AA Cost (Rs in Lakhs)	22.00
Total Cost of Completion/Expenditure Incurred ending 3/2022	13.00
Date of Start Month/Year	14-10-2021
Date of Completion	8-1-2022
No of Beneficiaries	230



Sr.no	63
Name of the work with Location	Landscaping at Bhaur Kulian
Department/Organization	JMC
Executive Agency	JMC
Block /District	JAMMU
AA Cost (Rs in Lakhs)	12.00
Total Cost of Completion/Expenditure Incurred ending 3/2022	7.76
Date of Start Month/Year	11-10-2021
Date of Completion	18-3-2022
No of Beneficiaries	250






Sr.no	64
Name of the work with Location	Landscaping adjoining Primary Health centre at bhour
Department/Organization	JMC
Executive Agency	JMC
Block /District	JAMMU
AA Cost (Rs in Lakhs)	12.00
Total Cost of Completion/Expenditure Incurred ending 3/2022	7.85
Date of Start Month/Year	11-10-2021
Date of Completion	17-3-2022
No of Beneficiaries	550



Sr.no	65
Name of the work with Location	Bathroom for ladies and shamshan Ghat chak Sardara Attar Singh ward no.73
Department/Organization	JMC
Executive Agency	JMC
Block /District	JAMMU
AA Cost (Rs in Lakhs)	3.00
Total Cost of Completion/Expenditure Incurred ending 3/2022	2.85
Date of Start Month/Year	26-2-2022
Date of Completion	22-3-2022
No of Beneficiaries	600




Sr. No.	66
Name of the work with Location	Upgradation of Shamshan Ghat at Bhagwati Nagar Jammu.
Department/Organization	JMC
Executing Agency	Chander Kant Mahajan
Block/District	
AA Cost (Rs. In Lakhs)	15.00
Total Cost of Completion/Expenditure incurred ending 3/2022(Rs. In Lakhs)	13.06
Date of Start (Month/Year)	
Date of Completion(Month/Year)	15-07-2021
No. of beneficiaries	

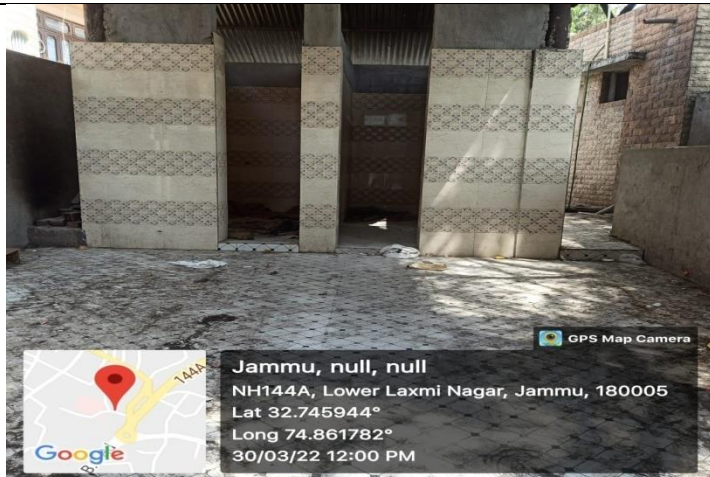

Sr. No.	67
Name of the work with Location	Construction of Tuttian / Ladies Bathroom near Dental College Jammu
Department/Organization	
Executing Agency	Karunesh Sharma
Block/District	
AA Cost (Rs. In Lakhs)	10.00
Total Cost of Completion/Expenditure incurred ending 3/2022(Rs. In Lakhs)	6.99
Date of Start (Month/Year)	16-10-2021
Date of Completion(Month/Year)	
No. of beneficiaries	



Sr. No.	68
Name of the work with Location	Construction of Turtian / Ladies Bathroom near Amphalla Jammu
Department/Organization	JMC
Executing Agency	Karunesh Sharma
Block/District	
AA Cost (Rs. In Lakhs)	4.00
Total Cost of Completion/Expenditure incurred ending 3/2022(Rs. In Lakhs)	2.68
Date of Start (Month/Year)	18-09-2021
Date of Completion(Month/Year)	
No. of beneficiaries	

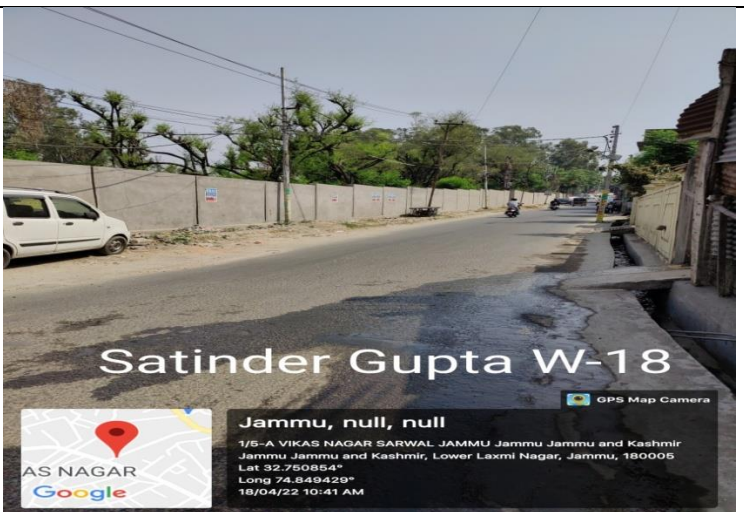

Sr. No.	69
Name of the work with Location	Upgradation of Turtian / Two Room and const. of Compound wall around Shishu Samadhiya at Vikas Nagar.
Department/Organization	JMC
Executing Agency	Satinder Gupta
Block/District	
AA Cost (Rs. In Lakhs)	20.00
Total Cost of Completion/Expenditure incurred ending 3/2022(Rs. In Lakhs)	17.32
Date of Start (Month/Year)	21-10-2021
Date of Completion(Month/Year)	07-01-2022
No. of beneficiaries	





Sr. No.	70
Name of the work with Location	Const. of waiting Shed at Shishu Samadhiya in Ward No.51
Department/Organization	JMC
Executing Agency	
Block/District	
AA Cost (Rs. In Lakhs)	6.50
Total Cost of Completion/Expenditure incurred ending 3/2022(Rs. In Lakhs)	4.43
Date of Start (Month/Year)	09-02-2022
Date of Completion(Month/Year)	08-03-2022
No. of beneficiaries	



Sr. No.	71
Name of the Work with location	Construction of officers Room in Town hall Complex, JMC Jammu, Town Hall Complex Jammu
Dept./ Organization	Jammu Municipal Corporation
Executing Agency	Projects Division, JMC
Block/District	Jammu
AA Cost (Rs. in Lacs)	8.12
Total cost of Completion/Expenditure incurred ending 03/2022 (Rs. in Lacs)	5.963
Date of START (MM/YYYY)	12/2021
Date of Completion (MM/YYYY)	03/2021
Number of Beneficiaries	10
