
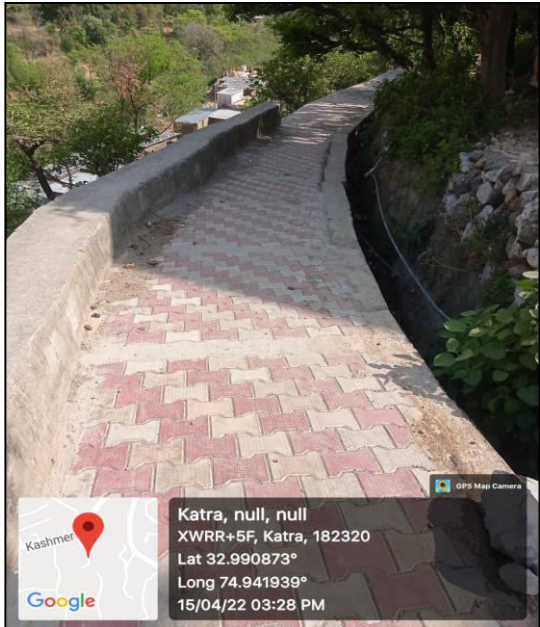
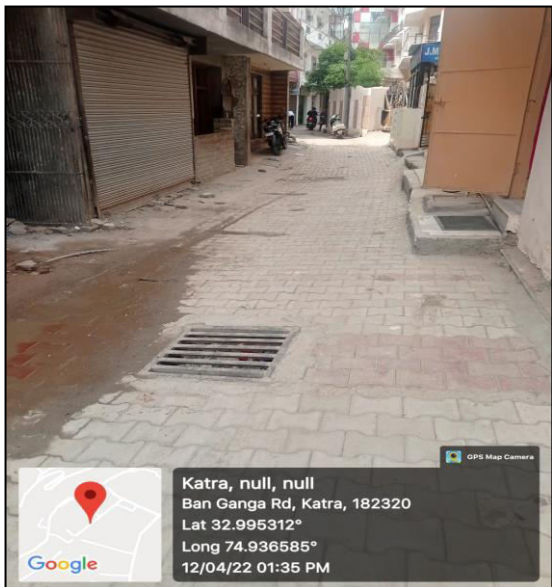


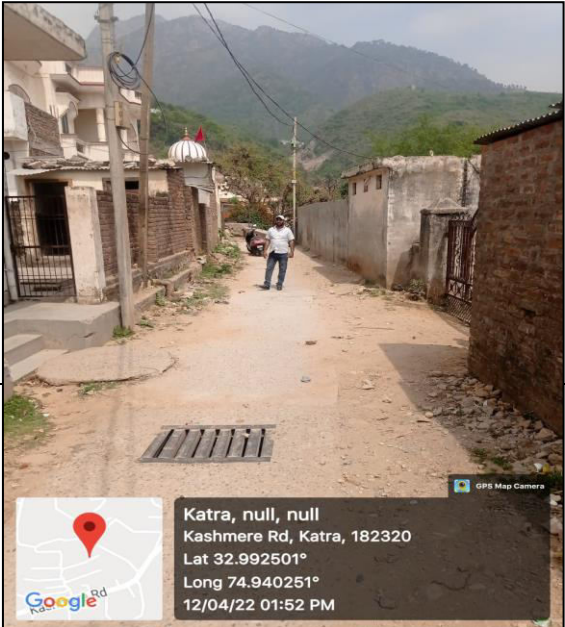

Format "C"
Geotaged Photograph (JPG) Format With Details
(Katra Development Authority)

	Work No.	01(UDS)
	Name of the work with Location	Construction of lane of Behro Mandir lane from house of sh. Romesh to house of Sh. Ratto. Ward no. 13 katra
	Department/Organization	Urban local bodies, office Municipal committee Katra
	Executive Agency	PWD (R&B) Katra
	Block /District	Katra/Reasi
	AA Cost (Rs. In Lakhs) :-	9.00 lacs
	Total Cost of Completion Expenditure incurred ending 3/2022	4.04 lacs
	Date of Start (Month/Year):-	
	Date of completion (Month/Year) :-MARCH 2022	12/2021
	No. of beneficiaries :-	400

	Work No.	02(UDS)
	Name of the work with Location	Repair and renovation of Lane and drain from House of Balwant Sarpanch to Dharmshalla , Ward no-7 ,MC ,Katra
	Department/Organization	Urban local bodies, office Munciple committee Katra
	Executive Agency	PWD (R&B) Katra
	Block /District	Katra/Reasi
	AA Cost (Rs. In Lakhs)	13.130 lacs
	Total Cost of Completion Expenditure incurred ending 3/2022	3.939 Lacs
	Date of Start (Month/Year)	NOV-2021
	Date of completion (Month/Year)	March 2022
	No. of beneficiaries :-	2000


	Work No.	03(UDS)
	Name of the work with Location	Balance work of Lane and Drain from House of Sh. Perma nand to house of Sh. Sanju Prasher, Ward no -9, MC, Katra
	Department/Organization	Department/Organization :- Urban local bodies, office Munciple committee Katra
	Executive Agency	PWD (R&B) Katra
	Block / District	Katra/Reasi
	AA Cost (Rs. In Lakhs)	3.00 lacs
	Total Cost of Completion Expenditure incurred ending 3/2022 :-	2.585Lacs
	Date of Start (Month/year)	11/2022
	Date of Completion (MM/YY)	03/2022
	No. of beneficiaries :-	500



	Work No.	04(UDS)
	Name of the work with Location	Construction of Lane and Drain from house of Sh . Sham Lal Bijliwala Ward no- 12, MC, Katra
	Department/Organization	Department/Organization :- Urban local bodies, office Municipal committee Katra
	Executive Agency	PWD (R&B) Katra
	Block / District	Katra/Reasi
	AA Cost (Rs. In Lakhs)	6.00 lacs
	Total Cost of Completion Expenditure incurred ending 3/2022 :-	2.99 lacs
	Date of Start (Month/year)	12/2021
	Date of Completion (MM/YY)	03/2022
	No. of beneficiaries :-	150


	Work No.	05 (UDS)
	Name of the work with Location	Repair of lane and drain Mohallah Surgal Ward no.3 Katra
	Department/Organization	M.C Katra
	Executive Agency	PWD (R&B) Katra
	Block / District	Katra/Reasi
	AA Cost Rs. In Lakhs	2.00 lacs
	Total Cost of Completion Expenditure incurred ending 3/2022	1.269
	Date of Start (Month/year)	11/2021
	Date of Completion (MM/YY)	01/2022
	No. of beneficiaries :-	100


Swachh Bharat Mission -Urban


	S.No.	1
	Name of the work with location	Construction of Community Toilet at Ambedkar Bhawan, W.No 1 Bari Brahmana
	Department/organization	Urban Local Bodies Jammu
	Executive Agency	XEN PWD(R&B) Division Samba
	Block / district	Samba
	AA cost (Rs in lacs)	10.50
	Total cost of Completion/expenditure incurred ending 03/2022	10.50
	Date of start (month / year)	10/11/2019
	Date of completion (month / year)	25/11/2021
	No of beneficiaries	675

	S.No.	2
	Name of the work with location	Construction of Community Toilet in Municipal Park at W No 3 NHAI, MC Bari Brahmana
	Department/organization	Urban Local Bodies Jammu
	Executive Agency	XEN PWD(R&B) Division- Samba
	Block / district	Samba
	AA cost (Rs in lacs)	10.50
	Total cost of Completion/	10.50

	expenditure incurred ending 03/2022	
	Date of start (month / year)	10/07/2020
	Date of completion (month / year)	05/07/2021
	No of beneficiaries	265
 <p>Latitude: 32.633555 Longitude: 74.904793 Elevation: 325.57±35 m Accuracy: 5.8 m Time: 03-14-2022 11:32 Note: ward no. 08 community toilet</p>	S.No.	3
	Name of the work with location	Construction of Community Toilet at Bassi Kalan Ward No 8 Bari Brahmana
	Department / organization	Urban Local Bodies Jammu
	Executive Agency	XEN PWD(R&B) Division-Samba
	Block / district	Samba
	AA cost (Rs in lacs)	10.50
	Total cost of Completion/ expenditure incurred ending 03/2022	10.50
	Date of start (month / year)	20/04/2019
	Date of completion (month / year)	23/10/2021
	No of beneficiaries	650
	S.No.	4
	Name of the work with location	Construction of Community Toilet at Kadgal Ward No 13 Bari Brahmana
 <p>Latitude: 32.633137 Longitude: 74.932138 Elevation: 330.06±28 m Accuracy: 27.5 m Time: 03-14-2022 11:59 Note: ward no. 13 community toilet</p>	Department / organization	Urban Local Bodies Jammu
	Executive Agency	XEN PWD(R&B) Division-Samba
	Block / district	Samba
	AA cost (Rs in lacs)	10.50
	Total cost of Completion/ expenditure incurred ending 03/2022	10.50
	Date of start (month / year)	26/12/2021
	Date of completion (month / year)	20/02/2021


 <p>Latitude: 32.606161 Longitude: 75.609089 Elevation: 722.99±100 m Accuracy: 23.0 m Time: 04-04-2022 10:19</p>	S.No.	5
	Name of the work with locations	Construction of Swachh Kendra (MRF) at MC Billawar (SBM)
	Department/ Organization	PWD (R&B)
	Executive Agency	PWD (R&B) Division Basohli
	Block / District	Billawar/ Kathua
	AA cost (Rs.in Lacs)	35.43 lac
	Total cost of completion expenditure incurred ending 03/2022	---
	Date of start (month / year)	01/2022
	Date of completion (Month / Year)	03/2022
	No. of beneficiaries	5000

 <p>Latitude: 32.606188 Longitude: 75.609172 Elevation: 738.99±100 m Accuracy: 8.5 m Time: 04-04-2022 10:18</p>	S.No.	6
	Name of the work with locations	Construction of compost pit under Swachh Bharat mission at MC Billawar (SBM)
	Department/ Organization	PWD (R&B)
	Executive Agency	PWD (R&B) Division Basohli
	Block / District	Billawar/ Kathua
	AA cost	12.32 lac
	Total cost of completion / expenditure incurred ending 03/2022	---
	Date of start	01/2022
	Date of completion	03/2022
	No.of beneficiaries	5000

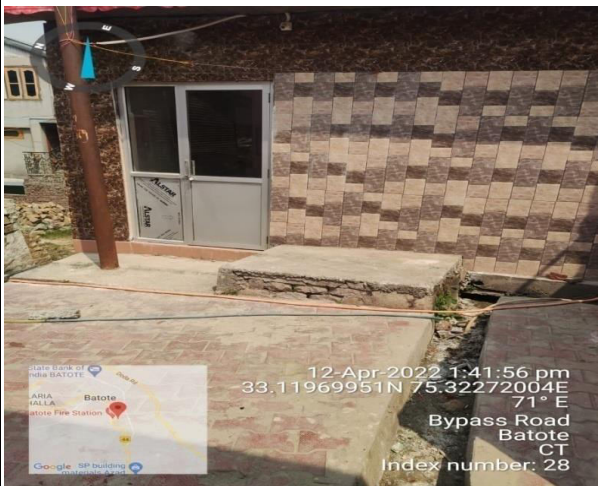
 <p>12-Apr-2022 1:41:56 pm 33.11969951N 75.32272004E 71° E Bypass Road Batote CT Index number: 28</p>	Name of the work with location	Constt. Of Community Toilet at Rani Talab Mandir Batote Ward No. 05
	Department/organization	M.C Batote
	Executing agency	PWD (R&B) Ramban
	Block/District	Batote
	AA Cost (Rs. In lacs)	13.559 Lacs
	Total Cost of Completion / Expdt. Incurred ending 03/2022	Nil
	Date of Start	2019-20
	Date of completion	Nil
	No of beneficiaries	500



S. No.	8
Name of the work with location	Const. of Community Toilet near Jamia Gholusia Anwar UI Islam Sukha Katha W. No. 1
Department/ organization	MC Poonch
Executive agency	PWD
Block /District	Poonch
AA Cost (Rs. In lakhs)	13.569
Total cost of completion/expenditure incurred ending 3/2022	0
Date of start	15-05-2018
Date of completion	20-02-2021
No. of beneficiaries	500 (per day)

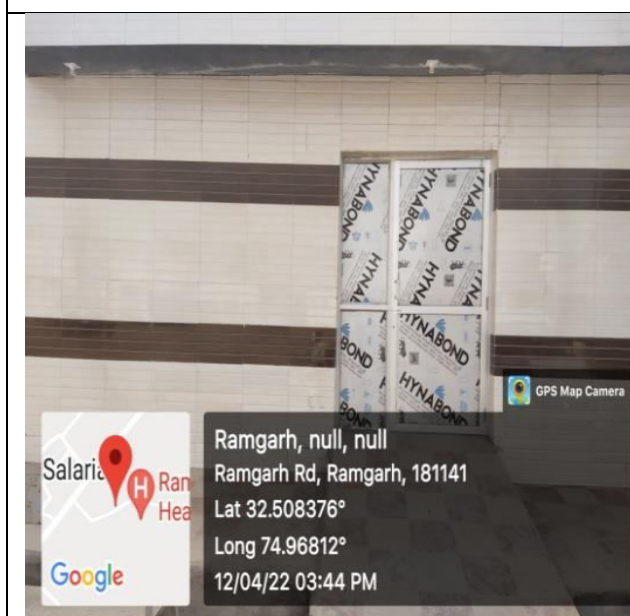

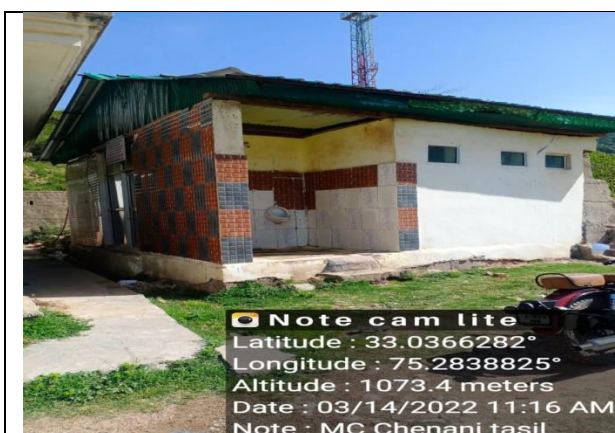

Name of work with Location	Construction of Community Toilet at Community Health Center Ramgarh
Department/ Organization	ULB / Municipal Committee Ramgarh
Executing Agency	Executive Engineer PWD (R&B)
Block/ District	Samba
AA Cost (Rs. In lacs)	10.5
Total Cost of Completion/Expenditure incurred ending 03/2022	0
Date of Start (Month/ Year)	2021-22
Date of Completion (Month/ Year)	Feb-22
No. of beneficiaries	650




Name of work with Location	Construction of Community Toilet near Tehsil office Complex Chenani
Department/ Organization	Municipal Committee Chenani
Executing Agency	DULBJ
Block/ District	Udhampur
AA Cost (Rs. In lacs)	13.59 Lac
Total Cost of Completion/Expenditure incurred ending 03/2022	---
Date of Start (Month/ Year)	---
Date of Completion	
No. of beneficiaries	1000 Approx

Drainage Sector

	S.No.	1
	Name of the work with location.	Const of Deep drain from Khour Camp to Shamshan Ghat Nallah
	Department/Organization	MC Khour
	Executing agency	XEN PWD-III Jammu
	Block/District	Jammu
	AA cost (Rs. In lakhs)	8,99,859/-
	Total cost of completion/Exp. Incurred ending 03/2022	2.00 lacs
	Date of Start (Month/year)	20-12-2021
	Date of completion	25-02-2022
	No. beneficiaries.	400 Nos.

	S.No	2
	Name of the work with Location	Construction of Nalla/Deep Drain and allied works at ward No. 05 Ghou Manhasan (Part-I , Phase-II)
	Department/ Organization	DULBJ/MC Ghou Manhasan
	Executive Agency	PWD(R&B) Div-III
	Block District	Jammu
	AA Cost (Rs.in lakhs)	27.50
	Total Cost of Completion/Expenditure incurred ending 03/2022	13.43 (CC1 only)
	Date of Start	08/2021
	Date of Completion	01/2022
	No. of beneficiaries	400-500 Approx

	S.No.	3
	Name of the work with locations	Construction of RCC walling from Mash=jid towards Nardian Bowli part 2 nd
	Department/ Organization	PWD (R&B)
	Executive Agency	PWD (R&B) Division Basohli
	Block / District	Billawar/ Kathua
	AA cost (Rs. in Lacs)	62 lac
	Total cost of completion exptn. Incurred ending 3/22	38.38
	Date of start	07/2021
	Date of completion	09/2021
	No. of beneficiaries	500




S. No.	4
Name of the work with location	Const. of Nallah with RCC slab at Mohalla Kamakhan in W. No. 7 near H/o Sham Singh, Warayam Singh Dushant Puri Poonch city.
Department/organization	MC Poonch
Executive agency	PWD
Block /District	Poonch
AA Cost	18.07
Total cost of compl /expnt. incurred ending 3/22	11.84
Date of start	12-01-2022
Date of completion	16-02-2022
No. of beneficiaries	500 (per day)




S. No.	5
Name of the work with location	Const. of RCC slab in W. No. 10 and its adjoining area.
Department/organization	MC Poonch
Executive agency	PWD
Block /District	Poonch
AA Cost	23.45
Total cost of completion/expenditure incurred ending 3/2022	17.00
Date of start	02-01-2022
Date of completion	20-02-2022
No. of beneficiaries	600 (per day)




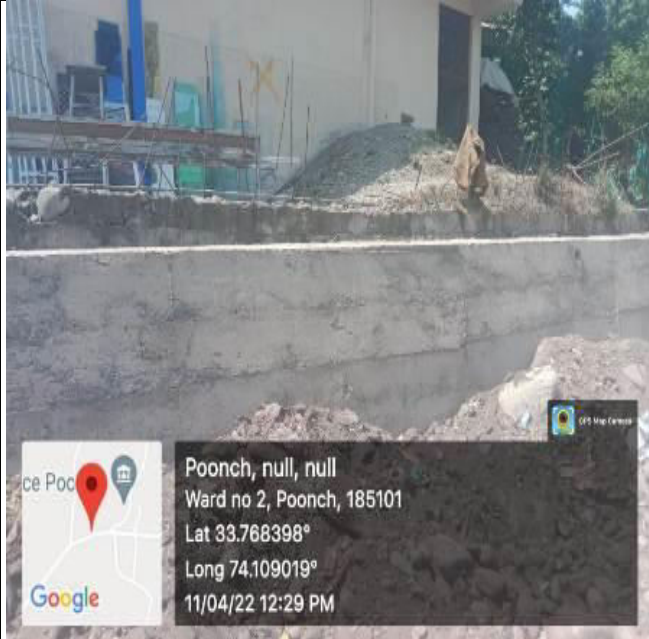
S. No.	6
Name of the work with location	Const. of Nallah walling on both side from main road to Masjid W. No. 01.
Department/organization	MC Poonch
Executive agency	PWD
Block /District	Poonch
AA Cost	28.57
Total cost of completion/expenditure incurred ending 3/2022	15.08
Date of start	30-12-2021
Date of completion	25-03-2022
No. of beneficiaries	500 (per day)

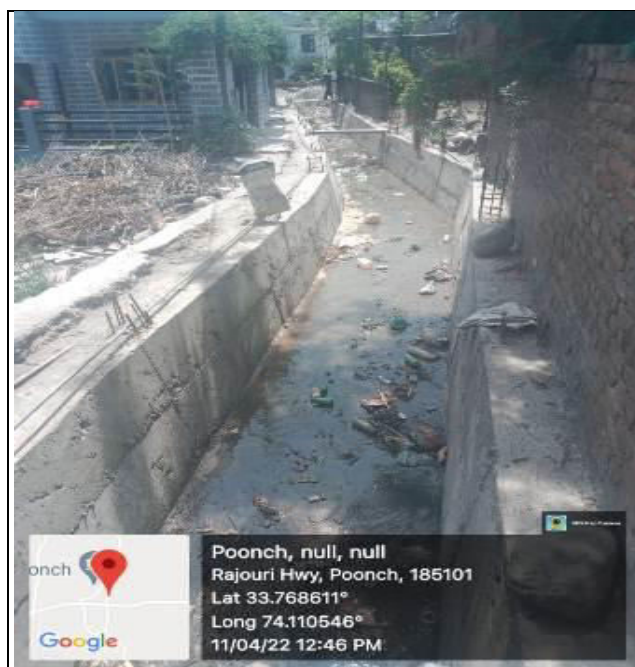

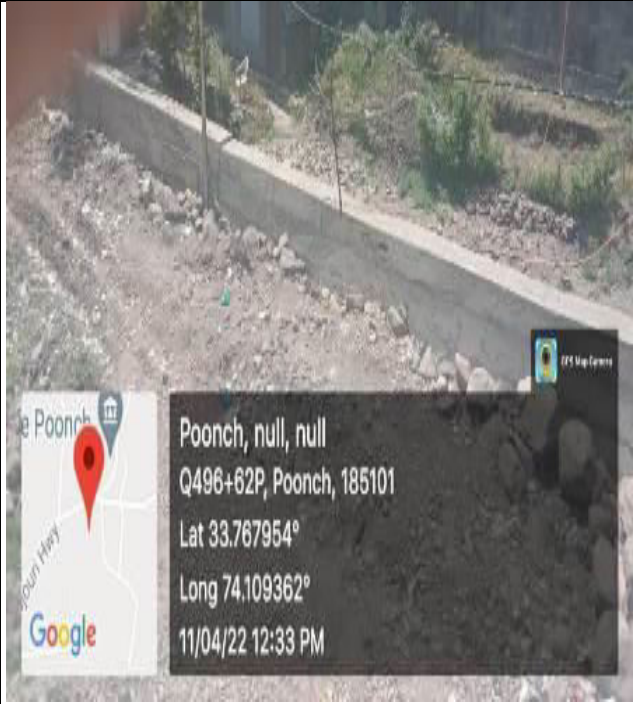

S. No.	7
Name of the work with location	Const. of a deep drain covering with RCC slab H/o Thakur Kulbir Singh to its flow in river Poonch Town.
Department/organization	MC Poonch
Executive agency	PWD
Block /District	Poonch
AA Cost	30.88
Total cost of completion/expenditure incurred ending 3/2022	11.12
Date of start	30-12-21
Date of completion	16-03-2022
No. of beneficiaries	300 (per day)

	S. No.	8
	Name of the work with location	Const. of Nallah walling on both side from crusher main road at Sukha Katha W. No. 1 Poonch Town (Fall to Down Side near culvert).
	Department/organization	MC Poonch
	Executive agency	PWD
	Block /District	Poonch
	AA Cost (Rs. In lakhs)	15.08
	Total cost of completion/expenditure incurred ending 3/2022	5.17
	Date of start	28-12-2021
	Date of completion	20-02-2022
	No. of beneficiaries	400 (per day)

	S. No.	9
	Name of the work with location	Const. of Nallah Walling on both side from main road concrete path and Edge Wall from Shop of Ajit Singh W. No. 1 MC Poonch.
	Department/organization	MC Poonch
	Executive agency	PWD
	Block /District	Poonch
	AA Cost (Rs. In lakhs)	15.72
	Total cost of completion/expenditure incurred ending 3/2022	5.54
	Date of start	15-02-2022
	Date of completion	15-03-2022
	No. of beneficiaries	450 (per day)


	S. No.	10
	Name of the work with location	Const. of P/Wall along Nallah side from H/o Tariq W. No. 1 Poonch
	Department/organization	MC Poonch
	Executive agency	PWD
	Block /District	Poonch
	AA Cost	13.65
	Total cost of completion/expenditure incurred ending 3/2022	6.38
	Date of start	15-03-2022
	Date of completion	26-03-2022
	No. of beneficiaries	600 (per day)


	S. No	11
	Name of the work with Location	Const. of Drain BGSBU Road and other on different locations.
	Department/ Organization	M.C Rajouri
	Executive Agency	PWD (R&B) Rajouri
	Block /District	Rajouri
	AA Cost	8.00
	Total expenditure incurred ending 03/ 2022	5.34
	Date of Start (Month/year)	01/2022
	Date of Completion (MM/YY)	03/2022
	No. of beneficiaries	450


 <p>Latitude: 33.995202 Longitude: 74.313427 Elevation: 975.48±9 m Accuracy: 7.3 m Time: 05-11-2021 16:54 Note: L/drain at Atti w.no 1 During execution</p>	S. No	02
	Name of the work with Location	Construction of Deep Drain at wards no 1 near the land of Zulfaqar& others.
	Department/Organization	M.C Rajouri
	Executive Agency	PWD (R&B) Rajouri
	Block /District	Rajouri
	AA Cost	4.00
	Total expenditure incurred ending 03/2022	1.897
	Date of Start	12/2021
	Date of Completion (MM/YY)	03/2022
	No. of beneficiaries	320


FC Grants


 <p>Ghou Manhasan, null, null PPFM+5GX, Bhagat Pur Upper, Ghou Manhasan, 181206 Lat 32.723211° Long 74.73398° 08/04/22 01:48 PM</p>	S.No	01
	Name of the work with Location	Installation for GYM equipments and children playground at GHSS Ghou Manhasan ward No. 07
	Department/Organization	DULBJ/MC Ghou Manhasan
	Executive Agency	PWD(R&B) Div-III
	Block District	Jammu
	AA Cost (Rs.in lakhs)	8.50
	Total Cost of Completion/Expenditure incurred ending 03/2022	5.95
	Date of Start (Month/Year)	12/2021
	Date of Completion (Month /Year)	02/2022
	No. of beneficiaries	800-1000 Approx


	Name of the work with location	Construction of Children's park and open Air Gym at Ward No. 06 , Municipal Council Ramban Mega Project
	Department/organization	H&UDD
	Executing Agency	PWD(R&B Ramban)
	Block/District	Ramban
	AA Cost (Rs in lakhs)	10.94
	Total cost of completion/Expenditure incurred ending 03/2022	0.00
	Date of start (month-year)	02/2022
	Date of completion (MM/YY)	03/2022
	No of beneficiaries	500

	Name of Work:-	Development of Children Park and open-air gym at MC parole
	Deptt/Orgn.:-	HU&DD (M.C Parole)
	Executing Agency: -	PWD (R&B)
	Block/Distt.:-	Parole, Distt. Kathua
	Total AA Cost:-	16.00 Lakhs
	Total Exp. Incurred:-	14.91 lakhs
	Date of Start (Month/Year): -	12/10/21
	Date of Completion: -	2021-22
	No. of Beneficiaries: -	Inhabitant of MC PAROLE


	Name of Work:-	Renovation of Office of Municipal Committee, Parole
	Deptt/Orgn.:-	HU&DD (M.C Parole)
	Executing Agency: -	PWD (R&B)
	Block/Distt.:-	Parole, Distt. Kathua
	Total AA Cost:-	8.00 Lakhs
	Total Exp. Incurred:-	7.42 lakhs
	Date of Start (Month/Year):-	28/08/21
	Date of Completion:-	2021-22
	No. of Beneficiaries: -	Office


LOCAL BODIES INSTITUTIONS – FC GRANTS (MEGA PROJECT) UT (SOS) Works		
	S.No.	1
	Name of work with Location	Const. of lane/drain from H/o Guddu Kharka to Shiv Mandir W No 12 Ramnagar
	Department/ Organization	Municipal Committee Ramnagar
	Executing Agency	Executive Engineer PWD (R&B)
	Block/ District	Ramnagar
	AA Cost (Rs. In lacs)	15.13
	Total Cost of Completion/ Expenditure incurred ending 03/2022	1167000/-
	Date of Start (Month/ Year)	10-12-2021
	Date of Completion (Month/ Year)	Completed
	No. of beneficiaries	800


 <p>Latitude: 32.626156 Longitude: 74.920399 Elevation: 325.0155 m Accuracy: 3.0 m Time: 06-04-2022 08:25 Note: Development of open air gym at municipal committee at MC Bari Brahmana</p>	S.No.	07
	Name of the work with location	Development of open Air Gym at MC Bari Brahmana
	Department / organization	Urban Local Bodies Jammu
	Executive Agency	XEN PWD(R&B) Division- Samba
	Block / district	Samba
	AA cost (Rs in lacs)	5.00
	Total cost of Completion/ expenditure incurred ending 03/2022	0
	Date of start (month / year)	01/03/2022
	Date of completion (month / year)	26/03/2022
	No of beneficiaries	260


 <p>Poonch, null, null Q39M+9W2, Poonch, 185101 Lat 33.768335° Long 74.084731° 08/02/22 01:40 PM</p>	S. No.	3
	Name of the work with location	Development of Children Park and open air Gym at W. No. 13 Guru Nanak Parak MC Poonch
	Department/organization	MC Poonch
	Executive agency	PWD
	Block /District	Poonch
	AA Cost (Rs. In lakhs)	13.50
	Total cost of completion/expenditure incurred ending 3/2022	9.31
	Date of start (Month/year)	12/10/2021
	Date of completion (Month/Year)	31-03-2022
	No. of beneficiaries	800 (per day)


 <p>Latitude: 32.605599 Longitude: 74.731872 Elevation: 273.5521 m Accuracy: 14.9 m Azimuth: 29° (NE) Pitch: 3.7° (0.7°) Time: 02-02-2022 12:32 Note: Fixing of Open air Gym at MC RS Pura</p>	Name of work	Development of children park and open Air Gym at MC RS Pura.
	Department/Organization	Urban Local Bodies Jammu
	Executive Agency	PWD (R&B) Div-1 Jammu
	Block/District	Jammu
	AA Cost (Rs. In lakhs)	13.50 lacs
	Total cost of completion/Expenditure incurred ending 3/2021	4.63 lacs
	Date of start (month /Year)	27.12.2021
	Date of completion (month/Year)	02.02.2022
	No. of beneficiaries.	1500


 <p>Latitude: 32.833955 Longitude: 74.585321 Elevation: 286.7523 m Accuracy: 1900.0 m Time: 30-11-2021 13:15 Note: open air gym jourian</p>	Sr. No.	4
	Name of the work with Location	Development of Children park and open air Gym at ward no. 5 Jourian
	Department/Organization	Urban Local Bodies/MC Jourian
	Executive Agency	PWD
	Block/District	Akhnoor
	AA Cost (Rs. In lakhs)	8.80
	Total Cost of Completion/Expenditure incurred ending 03/2022	512000/-
	Date of Start (Month/Year)	08/09/2021
	Date of Completion(Month/Year)	18/11/2021
	No. ob beneficiaries	500


 <p>Vijay Pore, --, -- Vijaypur, Vijay Pore, Lat 32°33'51"N, Long 75°0'57"E 04/04/2022 02:51 PM</p>	Name of the work with location: Development of Children's Park and Open Air Gym at MC Vijaypur	
	Department/ Organization	MC Vijaypur
	Executing Agency	PWD (R&B) Division Samba
	Block/District	Vijaypur/Samba
	AA Cost (Rs. In Lacs)	13.00 Lacs
	Total Cost of Compl/Expnt. Incurred Ending 03/2022	6,71,900/-
	Date of Start	19.01.2022
	Date of Completion	17.02.2022
	No. of Beneficiaries	700


 <p>Latitude: 32.382188 Longitude: 75.593881 Elevation: 352.35±5 m Accuracy: 39.6 m Time: 04-04-2022 13:04 Note: sinages of different types- ward no 6 lakh</p>	Sr. no.	1
	Name of the work with locations	Sinages of different types ward no. 6 Lakhanpur
	Department/Organization	M.C. Lakhanpur
	Executive Agency	P.W.D R&B Kathua
	Block / District	KeeriaGandial Kathua
	AA Cost (Rs. in lakhs)	Rs. 25 Lac.
	Total cost of completion/Expenditure incurred ending 3/2022	Rs. 24.89 Lac
	Date of Start	
	Date of Completion	Completed
	No. of beneficiaries	30000 per day


 <p>Ramgarh, null, null Ramgarh Rd, Ramgarh, 181141 Lat 32.511122° Long 74.968915° 13/04/22 04:08 PM</p>	Name of work with Location	Development of Children Park and open Air Gym at MC Ramgarh
	Department/ Organization	ULB / Municipal Committee Ramgarh
	Executing Agency	Executive Engineer PWD (R&B)
	Block/ District	Samba
	AA Cost (Rs. In lacs)	8.08
	Total Cost of Completion/ Expenditure incurred ending 03/2022	0
	Date of Start (Month/ Year)	2021-22
	Date of Completion (Month/ Year)	Mar-22
	No. of beneficiaries	450

 <p>Taroti, null, null Unnamed Road, Khour, 181202 Lat 32.82224° Long 74.510737° 01/04/22 03:20 PM</p>	Name of the work with location.	Development of Children's park and open Air Gym at Municipal Committee Khour
	Department/Organization	MC Khour
	Executing agency	XEN PWD-III Jammu
	Block/District	Jammu
	AA cost (Rs. In lakhs)	7,71,980
	Total cost of completion/Exp. 03/2022	1.16lacs
	Date of Start	09-11-2021
	Date of completion	15-12-2021
	No. beneficiaries.	300 Nos.


	Name of the work with location	Providing and Laying of tiles work and Const. of Covered Drain at Bus Stand Reasi
	Department/organization	URBAN LOCAL BODIES JAMMU
	Executing agency	PWD
	Block/District	REASI
	Estimated Cost (Rs. In lacs)	48.2
	Total Expdt. Incurred ending 03/2022	33.24
	Project initiation year	May-21
	Date of completion	Aug-21
	No of beneficiaries	200000


	Name of the work with location	Development of Childrens park and Open Air Gym at MC Samba
	Department/Organization	Urban Local Bodies Jammu
	Executing Agency	PWD R&B Division Samba
	Block/District	Samba
	AA Cost (Rs. In lakhs)	13.50 Lacs
	Total cost of completion/Expdt. Incurred ending 3/2022	07.00 lacs
	Date of Start (Month Year)	Mar-22
	Date of Completion	Mar-22
	No. of Beneficiaries	300 Nos. approx.


	Name of the work with location	Development of children park and open air gym, Ward No. 2, Nowshera.
	Department/Organization	
	Executive Agency	PWD (R&B)
	Block/District	Rajouri
	AA Cost (Rs. In lakhs)	15.87 lac
	Total cost of completion/expenditure incurred ending 03/2022	6.12 lac
	Date of start (Month/Year)	10/2021
	Date of completion (Month/Year)	In progress
	No. of beneficiaries	Whole town


	Name of work with Location	Fencing of two dumping sites for SWM at Sui Chakhar Udhampur
	Department/ Organization	Municipal Council Udhampur
	Executing Agency	Executive Engineer PWD (R&B)
	Block/ District	Udhampur
	AA Cost (Rs. In lacs)	34.00 Lacs (8.14 Lacs One Site)
	Total Cost of Completion/ Expenditure incurred ending 03/2022	7.163 Lacs (One Site Completed)
	Date of Start	15/08/21
	Date of Completion	One site Completed
	No. of beneficiaries	100000 approx

	Name of work with Location	Development of park at W.No.18 of M.C. Udhampur
	Department/ Organization	Municipal Council Udhampur
	Executing Agency	Executive Engineer PWD (R&B)
	Block/ District	Udhampur
	AA Cost (Rs. In lacs)	33.04 Lacs
	Total Cost of Completion/ Expenditure incurred ending 03/2022	8.00 Lacs
	Date of Start	28/02/22
	Date of Completion	Completed
	No. of beneficiaries	80

	Name of work with Location	Development of park at W.No.7 of M.C. Udhampur
	Department/ Organization	Municipal Council Udhampur
	Executing Agency	Executive Engineer PWD (R&B)
	Block/ District	Udhampur
	AA Cost (Rs. In lacs)	
	Total Cost of Completion/ Expenditure incurred ending 03/2022	
	Date of Start (Month/ Year)	28/02/22
	Date of Completion (Month/ Year)	Completed
	No. of beneficiaries	80

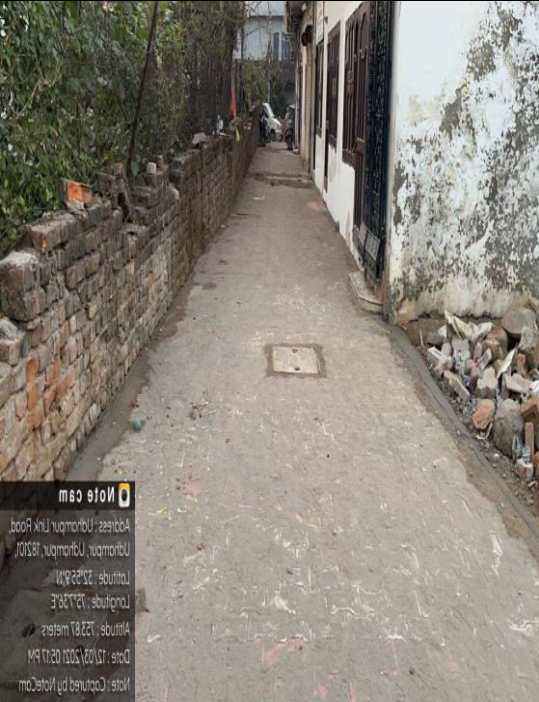	Name of work with Location	Const. of lane and drain from shop of Pawan Paba near forest Depot to the H.o Sanjeev Gupta W.no.12 Udhampur
	Department/ Organization	Municipal Council Udhampur
	Executing Agency	Executive Engineer PWD (R&B)
	Block/ District	Udhampur
	AA Cost (Rs. In lacs)	5.00 Lacs
	Total Cost of Completion/ Expenditure incurred ending 03/2022	4.208 Lacs
	Date of Start (Month/ Year)	12/10/21
	Date of Completion (Month/ Year)	03/12/21
	No. of beneficiaries	50 approx

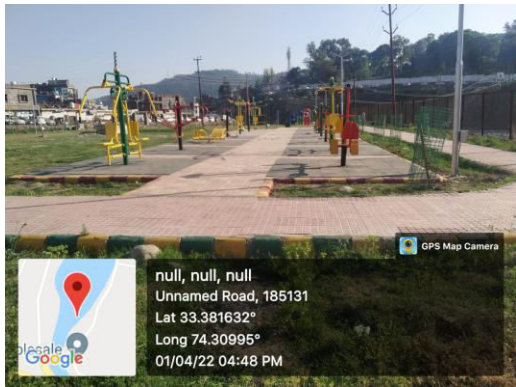	Name of the work with Location	Development of Children park & open air gym at MC Rajouri.
	Department/Organization	M.C Rajouri
	Executive Agency	PWD (R&B) Rajouri
	Block /District	Rajouri
	AA Cost (Rs. In lakhs)	25.00
	Total expenditure incurred ending 03/2022	18.18
	Date of Start	10/2021
	Date of Completion (MM/YY)	03/2022
	No. of beneficiaries	6000

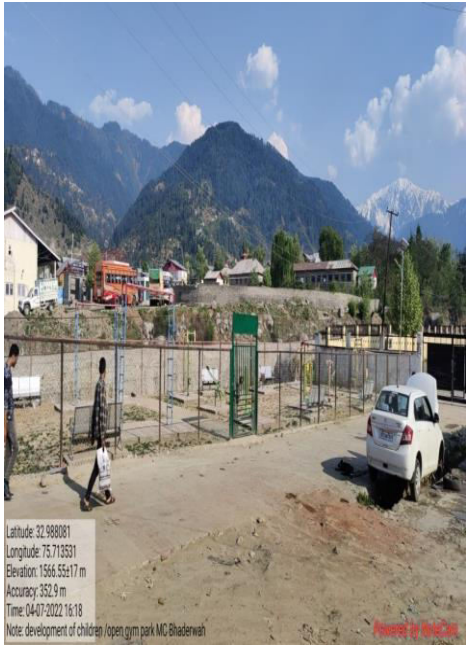	Name of the work with location:-	Constt. of children park and open gym system at MCB near Community hall Bhaderwah
	Department/Organization	Urban Local Bodies Jammu
	Executing Agency	PWD (R&B) Division Bhaderwah
	Block/ District	Bhaderwah/ Doda
	AA Cost (Rs. In Lakhs)	13.50
	Total Expdt incurred ending 03/2021	13.50
	Date of Start	Aug-21
	Date of Completion	Nov-21
	No. of beneficiaries.	200
